

HEALTHCONNECT CLINIC EXPERIENCE LAB

WEEK 4 PROJECT SUMMARY

Improving Patient Appointment Attendance and Healthcare Support Using Data and AI

Document Control

Track	Project Management
Project Phase	Initiation & Problem Understanding
Reporting Period	Week 4
Status	Initiation Baseline Established

1. WEEK 4 PROJECT FOCUS

Week 4 established the management foundation for the HealthConnect project by translating the broad business challenge into a defined project structure, delivery boundary and governance framework.

The focus was to establish how a multidisciplinary project involving data, AI, patient engagement and operational teams can be coordinated toward a common outcome.

The Project Management work therefore addressed six core areas:

Scope → Stakeholders → Work Structure → Dependencies → Risk → Communication

2. WORK COMPLETED

2.1 Project Definition

The Project Charter established the project's business context, problem statement, purpose, objectives, scope boundaries, success logic and delivery principles.

A key management position established during initiation is that data and AI are enabling capabilities rather than the definition of project success. The project will therefore be managed against its ability to create measurable patient and operational value.

2.2 Scope and Work Structuring

The project scope was defined to distinguish the activities required to address appointment attendance and patient-support challenges from activities outside the project's initial boundary.

The Work Breakdown Structure translated project objectives into structured work packages across the major delivery areas, creating a common basis for planning, ownership and subsequent scheduling.

2.3 Stakeholder Structure

The Stakeholder Register identified the principal groups affected by, contributing to or exercising authority over the project.

Stakeholders were assessed according to:

- Influence
- Decision authority
- Project impact
- Current engagement
- Required engagement
- Management strategy

This established the basis for targeted stakeholder management rather than treating all project participants as a single audience.

2.4 Risk and Dependency Position

The Initial Risk and Dependency Register identified the conditions most likely to affect delivery.

Key exposures include:

- Data availability and quality
- Limited understanding of operational workflows
- Cross-workstream dependencies
- Model reliability
- AI-generated response risks
- Scope expansion
- Lack of baseline performance measures
- Stakeholder adoption
- Workflow integration
- Over-reliance on technical performance

The dependency structure established the relationship between data readiness, analysis, solution development, intervention design, testing and implementation readiness.

2.5 Communication and Governance

A Communication Management Approach was established to control information flow across stakeholders and workstreams.

The framework defines:

- Information requirements
- Reporting cadence
- Decision management
- Escalation levels
- Communication ownership


- Information-control requirements
- Formal project records

This provides a mechanism for moving material information through:

Identification → Assessment → Decision → Action → Record

2.6 Integrated Project Position

The Week 4 outputs collectively establish an initial project control environment rather than independent documents. The relationship between the principal controls is:

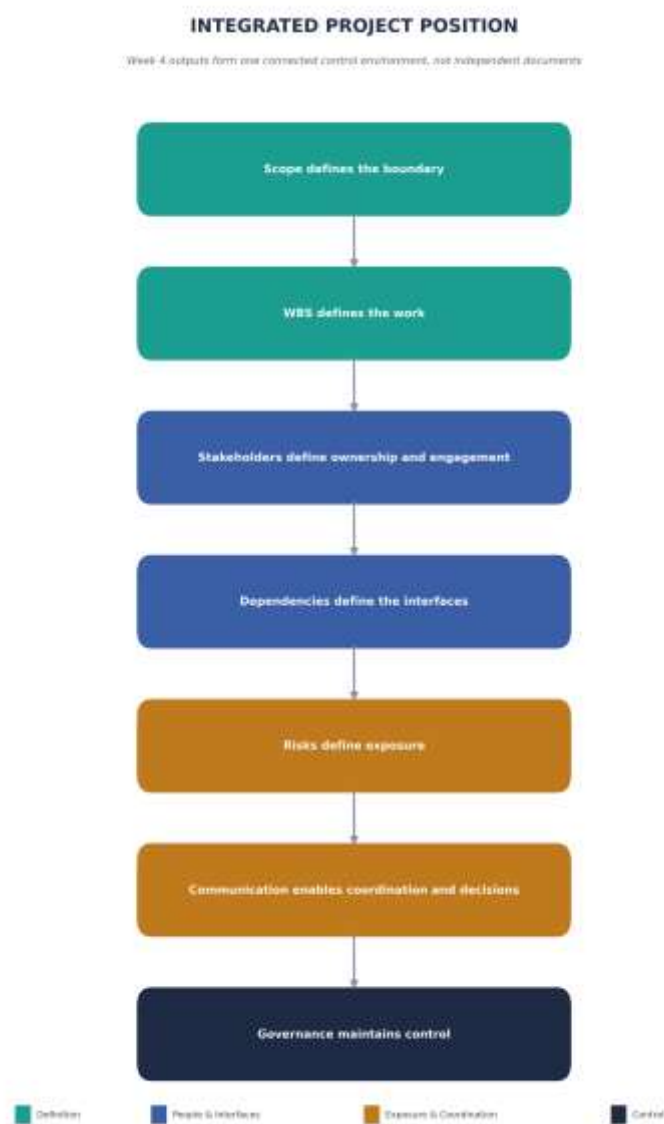

3. KEY PROJECT OBSERVATIONS

3.1 The project is dependency-driven

The major workstreams cannot progress independently. Data quality can affect analysis; analysis can affect predictive development; solution design can affect workflow integration; and validation can affect implementation readiness.

3.2 The problem requires an integrated response

Appointment non-attendance and patient-support challenges cannot be addressed through a single technical component. The project requires coordination between data, predictive intelligence, patient engagement, Generative AI, operational processes, testing and adoption.

3.3 Baseline evidence will be critical

The project currently has a defined problem but does not yet have validated baseline measures against which improvement can be quantified. Establishing those measures will be important before definitive performance targets are adopted.

3.4 Operational fit is a project requirement

A technically successful model or AI capability will not constitute project success if it cannot be incorporated into realistic clinic workflows.

3.5 Governance must remain embedded throughout delivery

Because some proposed capabilities may influence patient communication or intervention, human oversight, responsible AI, escalation and information controls must remain part of the delivery structure.

3.6 Scope discipline will be necessary

The healthcare context creates opportunities for additional use cases. Controlled scope management will therefore be necessary to maintain delivery focus and solution coherence.

4. PROJECT POSITION AT END OF WEEK 4

Project Control Area	Position
Project Definition	Established
Scope Boundary	Established
Stakeholder Structure	Established
Work Breakdown Structure	Established
Initial Risk Position	Established
Dependency Structure	Established
Communication Framework	Established
Governance Framework	Established
Delivery Roadmap	Established
Next Management Priority	Detailed planning, analysis coordination and solution-design readiness

Project Control Area	Position
OVERALL STATUS: Initiation baseline established; project ready to progress into the next planning and analysis cycle.	

5. WEEK 5 PROJECT FOCUS

Week 5 will move the project from “What are we solving and how will we govern it?” toward “What does the evidence tell us, what should be built, and how will we deliver it?”

The Project Management focus will be to establish the controls required for the next delivery cycle.

5.1 Requirement and Evidence Alignment

Clarify:

- Required information and data inputs
- Available evidence
- Unresolved information gaps
- Assumptions requiring validation
- Requirements sufficiently defined for progression

5.2 Detailed Work Planning

Translate the Week 4 WBS into detailed activities, ownership, sequencing and milestone requirements. Particular attention will be given to cross-workstream handoffs and activities that may become schedule constraints.

5.3 Dependency and Interface Management

Develop the high-level dependency structure into actionable controls covering:

- Dependency owner
- Required input
- Expected output
- Timing
- Downstream impact
- Resolution or contingency action

5.4 Risk Refinement

Reassess initial risks against emerging project evidence using:

Probability → Impact → Exposure → Response → Owner → Trigger

5.5 Solution-Design Coordination

Maintain alignment between emerging analytical findings and intervention concepts through:

5.6 Validation Planning

Define initial acceptance and validation considerations so future outputs can be assessed against both technical performance and operational usefulness.

5.7 Project Control Baseline


Establish the information required for detailed scheduling, milestone planning, resource coordination and delivery monitoring.

6. EXPECTED PROJECT POSITION AFTER WEEK 5

The project should progress from an initiation baseline toward an evidence-informed delivery baseline, with clearer visibility of:

- Validated requirements
- Detailed activities
- Workstream interfaces
- Activity dependencies
- Emerging schedule constraints
- Refined risks and responses
- Ownership and accountability
- Validation requirements
- Solution-design priorities
- Information required for subsequent development

The intended progression is:

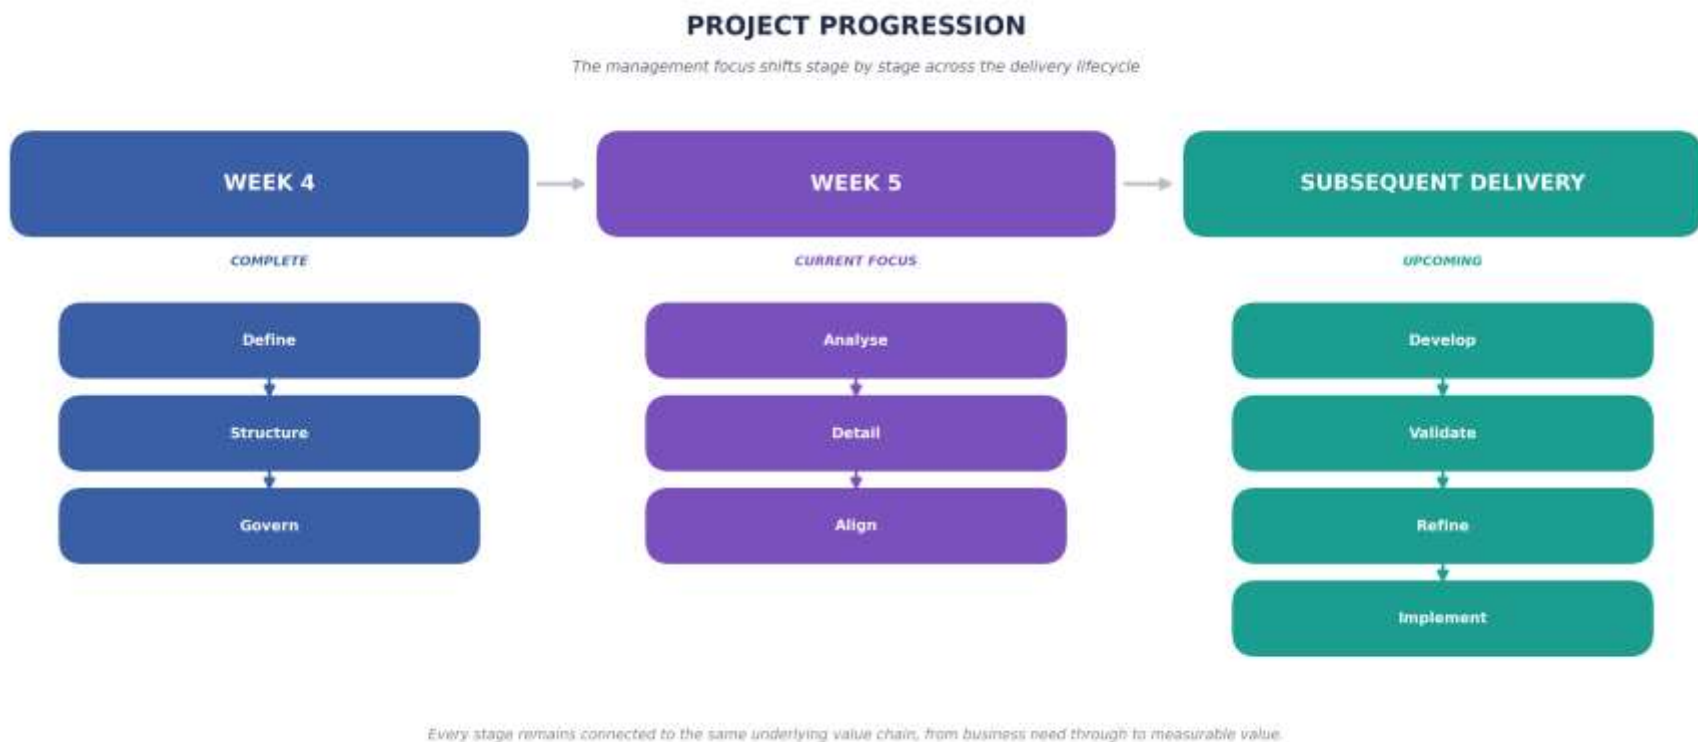

7. MANAGEMENT CONCLUSION

Week 4 established the structural foundation required to manage HealthConnect as an integrated project rather than a collection of independent technical activities. The immediate priority is now to test the assumptions behind the established baseline, strengthen delivery controls and convert the project structure into an actionable plan. The project will proceed on the basis that every major workstream remains connected to the same value chain:

Business Need → Patient Need → Evidence → Solution → Operational Adoption → Measurable Value

End of Week 4 Project Summary
