

ANALYSTLAB AFRICA
EXPERIENCE LAB INTERNSHIP PROGRAMME
HEALTHCONNECT CLINIC EXPERIENCE LAB
WEEK 7 CROSS-TRACK COORDINATION RECORD

Improving Patient Appointment Attendance and Healthcare Support Using Data and AI

Field	Detail
Project:	Improving Patient Appointment Attendance and Healthcare Support Using Data and AI
Programme:	AnalystLab Africa Experience Lab
Function:	Project Management
Reporting Period:	Week 7
Document Type:	Cross-Track Coordination Record
Document Status:	Controlled Working Record
Version:	2.0
Record Owner:	Project Management
Review Point:	Week 7 Cross-Track Integration & Validation Review
Overall Coordination Position:	AMBER-RED — MATERIAL INTERFACE DEPENDENCIES REMAIN OPEN

1. RECORD PURPOSE

This record establishes the formal project-management evidence trail for material coordination conducted across the HealthConnect workstreams during Week 7.

Its purpose is to establish, for each material interface:

- What coordination was required;
- Which workstreams were involved;
- What output, evidence or requirement was exchanged;
- What receiving-side action followed;
- Whether a resulting change can be demonstrated;
- What evidence supports the coordination;
- What remains unresolved; and
- What project-control action is required before downstream progression.

The record covers coordination involving:

- Data Analytics
- Data Science
- Machine Learning / ML Engineering
- Generative AI
- Project Management, where cross-track evidence affected integration, testing, risk, decisions, schedule or readiness.

The record is deliberately maintained at the coordination-control level.

It does not determine formal acceptance of an interface. That function is addressed through the Cross-Track Validation & Acceptance Matrix.


Coordination establishes that an interface was engaged and what occurred across it; validation establishes whether the exchanged output functions as intended; acceptance establishes whether the receiving context is prepared to rely upon it.

This record therefore does not treat communication, availability of an output, or a reported handoff as proof of integration.

2. COORDINATION CONTROL FRAMEWORK

2.1 Coordination Evidence Chain

The Week 7 coordination record applies the following control sequence:

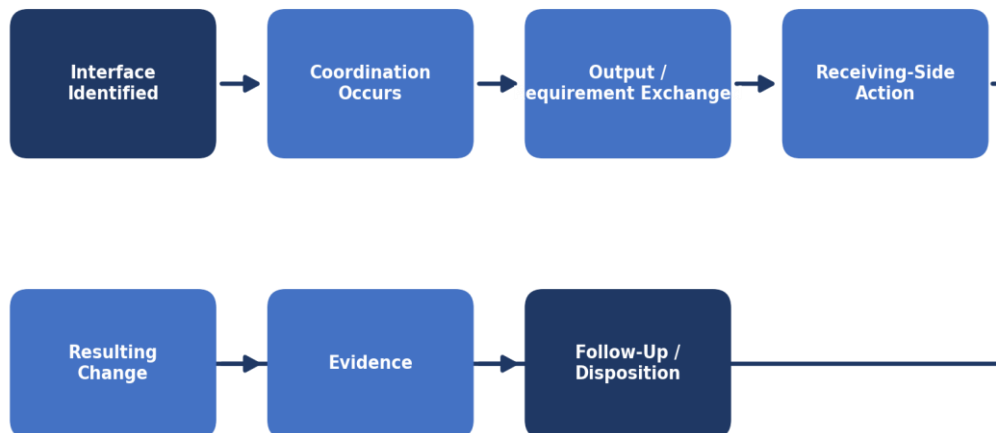

Not every interface will progress through every stage during the reporting period. Where a stage is not evidenced, the record preserves that gap rather than inferring completion.

2.2 Coordination Status Definitions

Status	Definition
Engaged	Material coordination occurred, but no defined output transfer has yet been established.
Transferred	A defined output, evidence package, requirement or input was provided to the receiving context.
Incorporated	The receiving workstream demonstrably used or acted upon the transferred information or output.
Integrated	The exchange resulted in a demonstrable downstream change within the receiving component or workflow.
Conditionally Integrated	Downstream technical use is evidenced, but a defined condition remains before the interface can be treated as fully accepted.
Pending Evidence	Coordination or exchange is established, but evidence of downstream use, resulting change or receiver disposition remains incomplete.
Blocked	Required coordination activity cannot proceed because a material prerequisite or external constraint is unresolved.
Not Activated	The interface was not required or activated during the reporting period.

Control Rule

No interface is classified as Integrated solely because communication occurred, an output was produced, or a handoff was reported.

Where receiving-side evidence is unavailable, the record retains the interface at the highest status objectively supported by the available evidence.

3. WEEK 7 MASTER COORDINATION REGISTER

Each interface record below captures the coordination objective, output/requirement exchanged, Week 7 activity, evidence/resulting change, status and required follow-up.

CTC-01 — Analytics → DS	
Coordination Objective	Make validated analytical evidence available for predictive development and maintain downstream traceability.
Output / Requirement Exchanged	Cleaned/validated/enriched dataset; EDA findings; no-show patterns; dashboard evidence; analytical interpretations.
Week 7 Coordination Activity	Analytical outputs remained available for downstream modelling and project review.

CTC-01 — Analytics → DS	
Evidence / Resulting Change	Source evidence established; specific DS incorporation and resulting model/feature change not fully evidenced.
Status	Pending Evidence
Required Follow-Up	Confirm receiving-side review, incorporation/disposition and resulting modelling implication.

CTC-02 — DS → ML	
Coordination Objective	Transfer and integrate the actual selected predictive candidate.
Output / Requirement Exchanged	Refined 33-feature Random Forest candidate; feature structure; preprocessing requirements; scoring requirements.
Week 7 Coordination Activity	DS established a refined candidate. ML exercised its integration pathway using a prior RF stand-in rather than the confirmed DS candidate.
Evidence / Resulting Change	ML pathway technically demonstrated; actual DS candidate transfer and execution not established.
Status	Pending Evidence
Required Follow-Up	Transfer actual candidate; reconcile schema/preprocessing; execute and verify.

CTC-03 — ML → Decision Path	
Coordination Objective	Establish a usable interface between model scoring and operational classification.
Output / Requirement Exchanged	Validated probability outputs; scoring interface; model-validation evidence.
Week 7 Coordination Activity	ML completed extensive technical testing and produced valid scoring outputs.
Evidence / Resulting Change	Technical scoring established; accepted operational interpretation and threshold not established.
Status	Conditionally Integrated
Required Follow-Up	Determine and formally accept threshold/classification logic.

CTC-04 — Decision Path → Intervention	
Coordination Objective	Convert an accepted risk classification into a defined operational response.
Output / Requirement Exchanged	Decision logic requirements; intended intervention pathway.

CTC-04 — Decision Path → Intervention	
Week 7 Coordination Activity	Downstream workflow requirement identified and controlled; no complete execution demonstrated.
Evidence / Resulting Change	Score→decision→intervention behaviour not yet evidenced.
Status	Pending
Required Follow-Up	Define, execute and verify the operational workflow.

CTC-05 — GenAI → PM / Governance	
Coordination Objective	Convert behavioural testing evidence into project-level control.
Output / Requirement Exchanged	Scenario results covering scheduling, emergency, diagnosis, treatment/medication, pricing and KB-grounding boundaries.
Week 7 Coordination Activity	PM reviewed evidence, carried findings into project controls and tracked refinement/retest requirements.
Evidence / Resulting Change	Behavioural evidence demonstrably affected testing, issue, risk and readiness control.
Status	Incorporated
Required Follow-Up	Continue control of outstanding safety, consistency and privacy validation.

CTC-06 — GenAI → Validation Environment	
Coordination Objective	Complete remaining scenario execution.
Output / Requirement Exchanged	Outstanding GenAI scenarios, including rash and Saturday-hours consistency scenarios.
Week 7 Coordination Activity	Two planned scenarios could not be executed because of Gemini 503/high-demand availability.
Evidence / Resulting Change	Execution constraint evidenced; scenarios remain untested rather than failed.
Status	Blocked
Required Follow-Up	Re-execute when the validation environment is available.

CTC-07 — GenAI → HealthConnect Support Workflow	
Coordination Objective	Establish sufficient behavioural alignment with the intended support context.
Output / Requirement Exchanged	KB-grounded responses; safety-boundary behaviours; scheduling and escalation behaviour.
Week 7 Coordination Activity	Selected behavioural boundaries were tested and one additional scheduling-urgency scenario was successfully validated.
Evidence / Resulting Change	Component evidence established; broader consistency, privacy and indirect emergency coverage remain incomplete.
Status	Conditionally Integrated
Required Follow-Up	Complete outstanding scenario coverage and disposition residual limitations.

CTC-08 — Analytics → PM / Project Control	
Coordination Objective	Convert analytical evidence into controlled project inputs.
Output / Requirement Exchanged	Dashboard evidence; no-show rate; segmented analytical findings and interpretations.
Week 7 Coordination Activity	PM incorporated available analytical evidence into project control records and retained the association-versus-causality boundary.
Evidence / Resulting Change	Direct PM incorporation evidenced.
Status	Integrated into PM Control
Required Follow-Up	Complete remaining dashboard/KPI validation and preserve interpretation controls.

CTC-09 — DS → PM / Project Control	
Coordination Objective	Translate predictive validation evidence into controlled integration and acceptance decisions.
Output / Requirement Exchanged	Candidate validation; CV performance; threshold robustness; segment results; feature analysis; overfitting assessment.
Week 7 Coordination Activity	PM incorporated DS evidence into testing, issue, risk, decision and readiness controls.
Evidence / Resulting Change	Predictive evidence is controlled; acceptance remains dependent on integration and operational decisions.
Status	Integrated into PM Control

CTC-09 — DS → PM / Project Control	
Required Follow-Up	Reassess following actual candidate integration and operationalisation.

CTC-10 — ML → PM / Project Control	
Coordination Objective	Establish the ML technical position as a project-controlled readiness input.
Output / Requirement Exchanged	Automated tests; batch scoring; reproducibility; negative testing; regression correction; backtesting; explainability.
Week 7 Coordination Activity	PM incorporated the technical evidence into project-level integration and readiness controls.
Evidence / Resulting Change	Strong technical evidence established; overall solution integration remains outstanding.
Status	Integrated into PM Control
Required Follow-Up	Reassess against the actual DS candidate and downstream workflow.

CTC-11 — All Workstreams → PM	
Coordination Objective	Consolidate material cross-track evidence into one controlled project position.
Output / Requirement Exchanged	Outputs; test evidence; dependencies; issues; decisions; readiness information.
Week 7 Coordination Activity	PM consolidated available evidence across workstreams into the Week 7 control set.
Evidence / Resulting Change	Project-level coordination position established and linked to schedule, risk, issue, decision and readiness controls.
Status	Integrated into PM Control
Required Follow-Up	Maintain through Week 8 integration and E2E validation.

4. INTERFACE COORDINATION RECORDS

4.1 CTC-01 — Data Analytics → Data Science

Coordination Objective

Provide the analytical evidence required to support predictive development while maintaining traceability between analytical findings and downstream modelling.

Material Exchange

The available Analytics output included:

- Cleaned, validated and enriched data;
- EDA across relevant appointment and patient-history dimensions;
- No-show behaviour findings;
- Six-KPI Power BI dashboard evidence; and
- Analytical interpretations.

The overall observed no-show rate was 48.46%.

Week 7 Coordination Position

The analytical evidence was available for downstream use and project review. However, the available evidence does not establish, input by input, which findings were incorporated into the DS model or what specific downstream artefact changed as a result.

Control Determination: Pending Evidence

Required Closure Evidence

1. Analytical inputs reviewed;
2. Incorporated, rejected or non-material findings;
3. Resulting model/feature implication; and
4. Supporting evidence.

Full closure of the Analytics→DS interface remains dependent on receiving-side disposition.

5. CTC-02 — DATA SCIENCE → ML ENGINEERING

Coordination Objective

Transfer the actual selected predictive candidate into the ML implementation pathway and verify compatibility.

Material Exchange

The intended interface comprises:

- Refined Random Forest candidate;
- 33-feature input structure;
- Preprocessing requirements;
- Model configuration; and
- Scoring requirements.

Week 7 Coordination Position

Data Science established a refined candidate through model validation and robustness assessment.

ML separately demonstrated that its model interface and scoring pathway could accept a Random Forest implementation.

The implementation used for that exercise was a stand-in and was not established as the final DS-selected candidate.


Control Determination

Interface Element	Evidence Position
DS candidate established	Yes
Candidate validation performed	Yes
ML interface technically exercised	Yes
Actual DS candidate transferred	Not evidenced
33-feature contract reconciled	Outstanding
Actual candidate executed through ML	Outstanding
Receiving-side acceptance	Outstanding

Status: Pending Evidence — Material Interface Dependency

Required Closure Evidence

The interface requires:

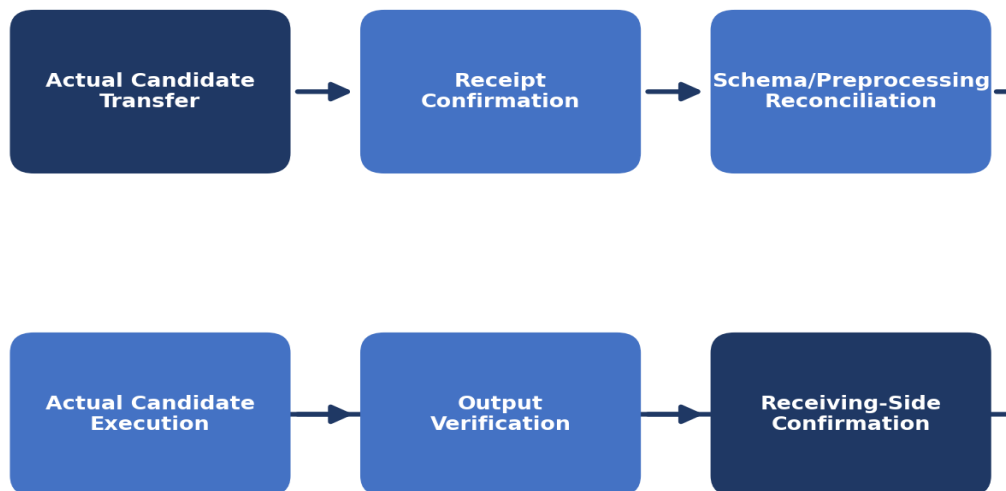

This remains one of the principal Week 7→Week 8 coordination dependencies.

6. CTC-03 — ML ENGINEERING → OPERATIONAL DECISION PATH

Coordination Objective

Establish whether technically generated model outputs can be interpreted consistently within the intended operational decision process.

Material Exchange

- model probability outputs;
- scoring interface;
- validation evidence;
- explainability evidence.

Week 7 Coordination Position

ML established substantial technical evidence, including:

- 69/69 automated tests passing;
- 948/948 records successfully scored;
- Valid probability outputs;
- Reproducibility testing;
- Negative-scenario testing;
- Correction and regression testing of the date-range defect;
- Expanding backtesting; and
- SHAP-based explainability.

Resulting Change

The scoring component progressed to a technically validated state.

The unresolved coordination requirement is the downstream interpretation of the score.

Control Determination: Conditionally Integrated

Required Closure Evidence

The operational chain must be explicitly established and tested:



The threshold remains an acceptance decision rather than an automatic technical consequence of model performance.

7. CTC-04 — DECISION PATH → INTERVENTION WORKFLOW

Coordination Objective

Establish the operational consequence of a validated risk classification.

Week 7 Coordination Position

The downstream interface has been identified as a required part of the HealthConnect value chain, but a complete score-to-decision-to-intervention execution has not been demonstrated.

Control Determination: Pending

Required Closure Evidence

- Accepted risk classification;
- Decision rule;
- Defined intervention;
- Workflow execution;
- Expected-versus-actual result; and
- Receiving-side confirmation.

This interface remains a prerequisite for full HealthConnect end-to-end validation.

8. CTC-05 — GENERATIVE AI → PM / GOVERNANCE

Coordination Objective

Translate GenAI test evidence into controlled project action rather than treating individual scenario results as standalone development evidence.

Material Exchange

Evidence included:

- Scheduling urgency;
- Emergency escalation;
- Diagnosis-related refusal;
- Treatment/medication boundaries;
- Pricing redirection; and
- Knowledge Base grounding.

Week 7 Coordination Position

PM incorporated material GenAI evidence into the Testing Activity Tracker, Integration & Issue Log, Risk & Dependency Register, Decision Log and readiness controls.

The previously identified emergency-disclaimer inconsistency was refined and re-tested.

One additional scenario:

“I need to be seen ASAP, is that possible?”

was successfully tested as scheduling urgency rather than a medical emergency.

Control Determination: Incorporated into PM Control

The coordination is therefore evidenced at the project-control level, while broader behavioural acceptance remains subject to the outstanding validation scope.

9. CTC-06 — GENERATIVE AI → VALIDATION ENVIRONMENT

Coordination Objective

Complete remaining scenario execution required to extend validation coverage.

Week 7 Position

Two planned scenarios could not be executed because the Gemini service returned 503/high-demand availability conditions.

The correct control classification is:

Blocked / Not Tested

The scenarios are not recorded as failed because no behavioural result was obtained.

10. CTC-07 — GENERATIVE AI → HEALTHCONNECT SUPPORT WORKFLOW

Coordination Objective

Establish whether the tested GenAI behaviour is sufficiently aligned with the intended HealthConnect support context.

Week 7 Position

Selected scenarios demonstrated expected behaviour across:

- Knowledge Base grounding;
- Emergency escalation;
- Diagnosis boundaries;
- Treatment/medication boundaries; and
- Scheduling urgency.

However, the evidence does not yet establish complete behavioural coverage for:

- Indirect or vague emergency phrasing;
- Broader response consistency;
- Privacy-sensitive scenarios; and
- Additional conversational conditions.

Control Determination: Conditionally Integrated

The component has usable evidence for selected behaviours but requires further validation before broader integrated acceptance.

11. CTC-08 — DATA ANALYTICS → PM / PROJECT CONTROL

Coordination Objective

Ensure that analytical evidence is reflected in project control without overstating its evidentiary strength.

Week 7 Coordination Activity

PM incorporated available analytical evidence into:

- Testing controls;
- Integration issues;
- Risks and dependencies;
- Decisions;
- Cross-track acceptance controls;
- Schedule controls; and

- Readiness assessment.

The analytical interpretation boundary has been retained: observed relationships are treated as descriptive/associational findings, not as demonstrated causal effects.

Control Determination: Integrated into PM Control

Remaining Requirement

Complete outstanding dashboard reconciliation/runtime validation and preserve the interpretation boundary in downstream modelling and intervention decisions.

12. CTC-09 — DATA SCIENCE → PM / PROJECT CONTROL

Coordination Objective

Translate model-development evidence and limitations into controlled project decisions.

Material Evidence

The DS evidence incorporated into project control includes:

- Refined Random Forest candidate;
- 5-fold stratified cross-validation;
- Threshold robustness testing;
- Segment performance;
- Feature ablation;
- Overfitting assessment; and
- Independent validation evidence.

Current evidence includes:

- 5-fold ROC-AUC: 0.6771 ± 0.0090
- Refined-model ROC-AUC: 0.6668
- Recall: 0.6742
- Train/test ROC-AUC gap: 0.0571

Week 7 Coordination Position

PM has incorporated these findings into the project-level acceptance and risk position.

The evidence supports candidate evaluation, but does not by itself establish final operational acceptance.

Control Determination: Integrated into PM Control

Remaining Requirement

Final disposition depends on actual DS→ML integration, model acceptance, threshold determination and downstream workflow validation.

13. CTC-10 — ML ENGINEERING → PM / PROJECT CONTROL

Coordination Objective

Convert ML's technical evidence into a controlled project-level readiness position.

Material Evidence

The PM control position incorporates:

- Automated test results;
- Batch-scoring evidence;
- Reproducibility;
- Negative testing;
- Regression correction;
- Expanding backtesting;
- Explainability; and
- Technical pipeline validation.

Week 7 Coordination Position

ML provides the strongest current technical validation evidence within the workstream set.

However, PM has explicitly separated:

Technical ML Readiness vs. Overall HealthConnect Integration Readiness

Control Determination: Integrated into PM Control

Remaining Requirement

Reassess after the actual DS candidate is integrated and the operational decision pathway is validated.

14. CTC-11 — ALL WORKSTREAMS → PM

Coordination Objective

Maintain one controlled project position from distributed workstream evidence.

Week 7 Coordination Activity

PM consolidated available evidence relating to:

- Outputs;
- Handoffs;
- Testing;
- Issues;
- Dependencies;
- Decisions;
- Limitations;
- Acceptance conditions; and
- Readiness.

The resulting evidence informed the updated timeline, Testing Activity Tracker, Integration & Issue Log, Risk & Dependency Register, Decision Log, Cross-Track Validation & Acceptance Matrix, Testing Progress & Status Report and Week 8 Readiness Assessment.

Control Determination: Integrated into PM Control

Remaining Requirement

Continue maintaining the record through Week 8 until material interfaces reach documented acceptance or formal residual disposition.

15. CROSS-TRACK COORDINATION CONTROL POSITION

Interface	Coordination Position	Primary Control Consequence
Analytics → DS	Evidence available; receiver-side disposition incomplete	Downstream traceability remains open
DS → ML	Actual candidate handoff not evidenced	Critical integration dependency
ML → Decision	Technical scoring established; operational rule unresolved	Acceptance condition remains open
Decision → Intervention	Workflow not demonstrated	E2E validation cannot yet proceed
GenAI → PM	Evidence incorporated into project controls	Governance linkage established
GenAI → Validation	Two scenarios blocked by service availability	Validation evidence incomplete
GenAI → HealthConnect	Selected behaviours evidenced; broader coverage incomplete	Conditional integration position
All Workstreams → PM	Consolidated project control established	Week 8 coordination baseline established

16. COORDINATION EVIDENCE MATURITY

Week 7 coordination should be interpreted across four distinct evidence levels:

Level	Evidence Standard	Week 7 Position
1 — Engagement	Relevant workstreams interacted around a defined requirement or output.	Established
2 — Transfer	A defined output, evidence package or requirement crossed the interface.	Partially established
3 — Downstream Use	Receiving workstream demonstrably used the transferred material and resulting change is identifiable.	Incomplete across critical interfaces
4 — Integrated Acceptance	Receiving-side use is validated and the interface is accepted for its intended downstream purpose.	Not established across the critical end-to-end chain

This maturity model is a coordination-control device, not a performance ranking of the individual workstreams.

17. OUTSTANDING COORDINATION ACTION REGISTER

Action ID	Interface	Required Action	Owner	Dependency / Trigger	Status
CCA-01	Analytics → DS	Confirm downstream review, incorporation or disposition of material analytical findings.	Analytics / DS	Analytical evidence available	Open
CCA-02	DS → ML	Transfer actual selected candidate and confirm receipt.	DS / ML	Candidate established	Open
CCA-03	DS → ML	Reconcile 33-feature structure and preprocessing requirements.	DS / ML	CCA-02	Open
CCA-04	DS → ML	Execute actual DS candidate through ML and record technical result.	ML / DS	CCA-02, CCA-03	Open
CCA-05	ML → Decision	Determine and formally accept operational classification threshold.	DS / PM	Candidate/model evidence	Open
CCA-06	Decision → Intervention	Define and test score-to-decision-to-intervention pathway.	PM / Relevant Tracks	CCA-05	Open
CCA-07	Analytics → PM	Complete KPI reconciliation and dashboard interaction validation.	Analytics	Dashboard runtime access	Open
CCA-08	GenAI → Validation	Re-execute scenarios blocked by service availability.	GenAI	Environment availability	Blocked
CCA-09	GenAI → HealthConnect	Complete broader emergency, consistency and privacy-sensitive validation.	GenAI	Approved scenarios	Open
CCA-10	All Interfaces	Obtain receiving-side disposition for material cross-track outputs.	Relevant Tracks / PM	Upstream evidence	Open
CCA-11	All Tracks	Execute HealthConnect end-to-end workflow validation.	All Tracks / PM	Critical interfaces cleared	Pending
CCA-12	PM	Reconcile coordination outcomes with risks, issues, decisions and schedule.	PM	CCA-01–CCA-11	In Progress

18. CONTROL-RECORD TRACEABILITY

The Cross-Track Coordination Record interfaces with the wider PM control set without replacing it:

Record	Control Function
Cross-Track Coordination Record	Records what was coordinated, exchanged, acted upon and followed up.
Cross-Track Validation & Acceptance Matrix	Determines whether material interfaces satisfy validation and acceptance conditions.
Testing Activity Tracker	Records individual tests, findings, actions and retests.

Record	Control Function
Integration & Issue Log	Controls materialised integration conditions requiring corrective action or disposition.
Risk & Dependency Register	Controls potential project consequences and dependency exposure.
Decision Log	Controls material decisions and unresolved acceptance positions.
Updated Project Timeline & Schedule Control	Controls sequencing, dependencies and progression.
Testing Progress & Status Report	Consolidates testing evidence into management status.
Week 8 Readiness Assessment	Determines controlled progression and readiness conditions.

The records are therefore linked rather than duplicated.


19. WEEK 7 COORDINATION DETERMINATION

AMBER-RED — MATERIAL INTERFACE DEPENDENCIES REMAIN OPEN

Week 7 demonstrates substantive coordination across the HealthConnect workstreams, with a clear progression from workstream-level output exchange toward testing, refinement, technical verification and project-level control.

The principal coordination limitation is no longer whether workstreams are active. It is whether the outputs have successfully crossed their intended interfaces and produced evidenced downstream use and acceptance.

The controlling sequence remains:

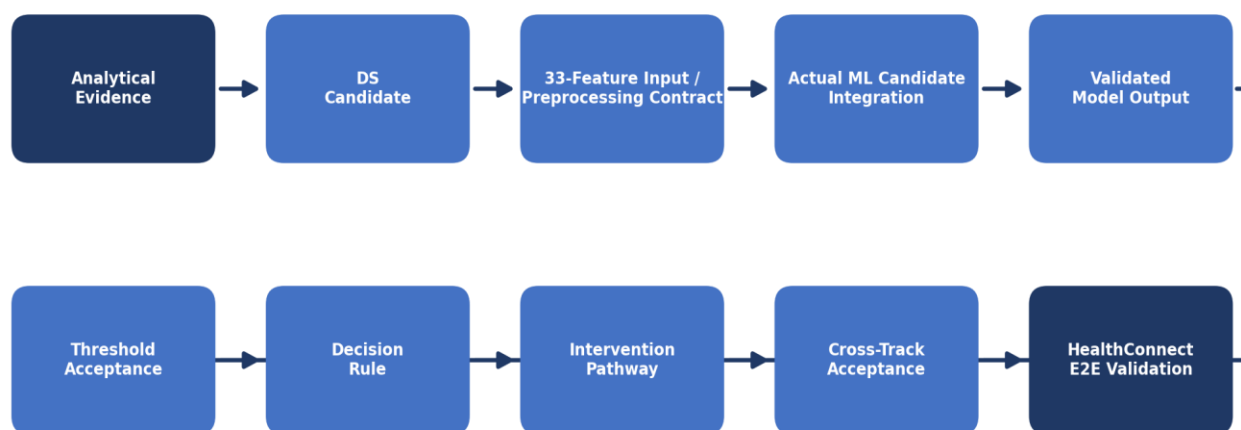

The most material open coordination conditions are:

- Incomplete receiver-side disposition of Analytics evidence;
- Absence of evidenced transfer and execution of the actual DS-selected candidate within ML;

- Unresolved operational classification threshold;
- Undefined/unvalidated score-to-intervention pathway;
- Incomplete GenAI safety, consistency and privacy coverage;
- Two GenAI scenarios blocked by service availability; and
- Absence of full HealthConnect end-to-end validation.

Accordingly, the Week 7 coordination position is:

Coordination is materially established across the project, but critical interfaces have not yet achieved complete downstream evidence and acceptance.

Week 8 progression may therefore proceed under the established controlled conditions; however, coordination status must not be represented as final integration, operational acceptance or end-to-end solution validation.

20. GOVERNANCE AND MAINTENANCE

Control	Requirement
Record Owner	Project Management
Update Authority	Project Management, based on documented workstream evidence and receiving-side confirmation
Review Frequency	Each material cross-track checkpoint and at the Week 8 integration review
Update Triggers	New handoff; receiver confirmation; downstream use; integration test; retest; material issue; acceptance decision; dependency change; readiness impact
Evidence Basis	Workstream output, documented exchange, receiver confirmation, test evidence, issue/decision record or other traceable project artefact
Status Control	Status may only advance when the evidence supporting the next coordination state is available
Escalation Route	See chain below
Closure Basis	Required coordination completed; downstream action demonstrated; resulting condition evidenced; unresolved limitation dispositioned; relevant receiving-side position recorded
Cross-References	Testing Activity Tracker; Integration & Issue Log; Risk & Dependency Register; Decision Log; Cross-Track Validation & Acceptance Matrix; Testing Progress & Status Report; Updated Project Timeline; Week 8 Readiness Assessment

21. VERSION CONTROL

Version	Phase	Change
V1.0	Week 6	Initial Cross-Track Coordination Record established from verified Week 6 coordination evidence.
V2.0	Week 7	Rebased for controlled Week 7 execution; incorporated testing and refinement evidence, actual interface positions, receiving-side evidence gaps, operationalisation dependencies, GenAI availability constraints, cross-track action controls and Week 8 progression requirements.

Next Formal Review

Week 8 Cross-Track Integration Checkpoint, or earlier where a material coordination condition affects integration, testing, safety, dependency management, schedule progression or readiness.
