

ANALYSTLAB AFRICA
EXPERIENCE LAB INTERNSHIP PROGRAMME
HEALTHCONNECT CLINIC EXPERIENCE LAB
WEEK 7 DECISION LOG


Improving Patient Appointment Attendance and Healthcare Support Using Data and AI

Field	Detail
Project:	Improving Patient Appointment Attendance and Healthcare Support Using Data and AI
Programme:	AnalystLab Africa Experience Lab
Workstream:	Project Management
Phase:	Week 7 — Testing, Refinement & End-to-End Validation
Version:	2.1
Status:	Controlled Working Log
Log Owner:	Project Management
Decision Basis:	Validated test evidence, integration findings, risk exposure, cross-track dependencies and Week 8 entry conditions

1. DECISION CONTROL FRAMEWORK

This log records material project decisions and unresolved decision requirements arising from Week 7 testing, integration and validation.

The decision-control chain is:

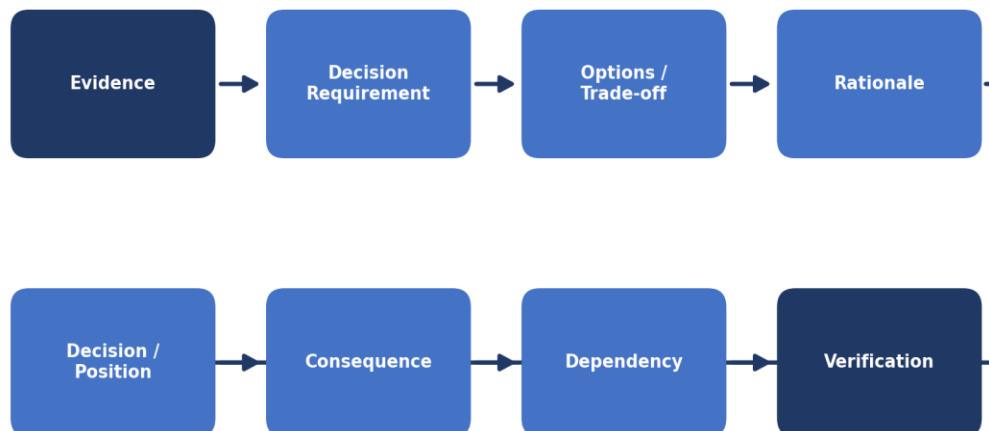

Where evidence or authority is insufficient, the decision remains Pending Decision rather than being inferred from workstream completion.

2. DECISION STATUS

Status	Definition
Approved	Decision formally accepted for implementation.
Conditionally Approved	Position accepted subject to explicit conditions or verification.
Pending Decision	Decision requirement identified but evidence, authority or acceptance remains outstanding.
Deferred	Decision intentionally postponed pending a defined dependency.
Rejected	Proposed position not accepted; alternative treatment required.
Superseded	Replaced by a subsequent controlled decision.

3. CONTROLLED DECISION REGISTER

Each decision record below captures the driver/evidence, decision required, options and trade-off, rationale, current position, consequence/dependency, verification requirement and control references.

DEC-001 — DS → ML Candidate Integration (Integration)	
Date / Required By	TBC / Before candidate integration
Owner / Authority	DS / ML; PM coordination
Impacted Tracks	DS, ML, PM
Decision Driver / Evidence	Refined RF candidate defined; ML interface tested, but the actual DS-selected candidate has not yet been transferred and executed through the ML pipeline.
Decision Required	Confirm the model artifact/version to be treated as the controlled integration candidate.
Options & Trade-off	Integrate current candidate: advances validation but requires interface confirmation. Defer: preserves assurance but delays downstream testing.
Rationale	Integration acceptance requires evidence that the intended DS candidate, rather than a stand-in, has crossed the interface successfully.
Current Position	Pending transfer, receipt, configuration and execution.
Consequence / Dependency	Blocks confirmation of actual DS→ML compatibility. Depends on DEC-002.
Verification / Closure	Evidence of candidate receipt, configuration and successful execution.
Control References	IIL-001; TA-019; R-001

DEC-001 — DS → ML Candidate Integration (Integration)	
Status	Pending Decision

DEC-002 — 33-Feature Input Contract (Interface / Technical Acceptance)	
Date / Required By	TBC / Before candidate execution
Owner / Authority	DS / ML
Impacted Tracks	DS, ML
Decision Driver / Evidence	Candidate defined around 33 features; feature order, preprocessing and ML input compatibility remain unverified.
Decision Required	Confirm the 33-feature structure and preprocessing as the controlled model input contract.
Options & Trade-off	Reconcile then accept: stronger interface assurance. Proceed without reconciliation: faster but increases compatibility exposure.
Rationale	The receiving pipeline must reproduce the input conditions under which the candidate was validated.
Current Position	Pending schema and preprocessing reconciliation.
Consequence / Dependency	Required before controlled candidate execution; depends on DEC-001.
Verification / Closure	Reconciled schema/preprocessing and successful scoring.
Control References	IIL-002; TA-011; R-001
Status	Pending Decision

DEC-003 — Classification Threshold (Operational Acceptance)	
Date / Required By	TBC / Before E2E
Owner / Authority	PM / DS / relevant decision authority
Impacted Tracks	DS, ML, PM
Decision Driver / Evidence	Independent threshold testing produced approximately 0.83 recall and 0.56 precision at the tested threshold.
Decision Required	Determine the threshold governing operational risk classification.

DEC-003 — Classification Threshold (Operational Acceptance)	
Options & Trade-off	Lower threshold: greater sensitivity with potentially more false alerts. Higher threshold: fewer alerts but potentially lower recall.
Rationale	Threshold selection determines the operating trade-off between identifying risk and generating intervention workload; it is therefore an acceptance decision, not merely a model parameter.
Current Position	Pending formal acceptance and configuration.
Consequence / Dependency	Required before a model score can drive a controlled operational decision. Depends on DEC-001/002.
Verification / Closure	Approved threshold, documented rationale, configuration and E2E verification.
Control References	IIL-003; TA-010; R-002
Status	Pending Decision

DEC-004 — Score → Decision → Intervention (Operationalisation)	
Date / Required By	TBC / Before Week 8 readiness
Owner / Authority	PM / ML / relevant operational owner
Impacted Tracks	ML, PM, Integrated Solution
Decision Driver / Evidence	Technical scoring is validated, but the complete pathway from score to classification, decision and intervention has not been demonstrated.
Decision Required	Define and accept the operational action pathway.
Options & Trade-off	Define and validate now: establishes testable operational value. Defer: preserves technical progress but leaves solution value unvalidated.
Rationale	A predictive output is not an operational outcome until a controlled action pathway is established.
Current Position	Pending pathway definition and validation.
Consequence / Dependency	Blocks demonstration of the complete operational value chain. Depends on DEC-003 and final candidate integration.
Verification / Closure	Successful score → decision → intervention test with documented expected/actual behaviour.
Control References	IIL-004; TA-020; R-002
Status	Pending Decision

DEC-005 — Analytics Evidence Acceptance (Evidence Governance)	
Date / Required By	TBC / Before downstream acceptance
Owner / Authority	Analytics / PM
Impacted Tracks	Analytics, DS, PM
Decision Driver / Evidence	Dashboard and EDA evidence available; KPI reconciliation, interaction testing and downstream disposition remain incomplete.
Decision Required	Determine whether analytical outputs meet the evidence standard for downstream reliance.
Options & Trade-off	Conditional acceptance: allows controlled use with stated limitations. Defer: stronger assurance but delays downstream reliance.
Rationale	Output availability does not establish calculation, interaction and downstream acceptance.
Current Position	Pending reconciliation and disposition.
Consequence / Dependency	Limits downstream reliance until outstanding evidence is resolved.
Verification / Closure	KPI reconciliation, runtime interaction evidence and receiving-track disposition.
Control References	IIL-005–IIL-007; TA-002–TA-006; R-003
Status	Pending Decision

DEC-006 — Analytical Interpretation Boundary (Analytical Governance)	
Date / Required By	Week 7
Owner / Authority	Analytics / PM
Impacted Tracks	Analytics, DS, PM
Decision Driver / Evidence	EDA identifies differences across demographic, temporal, distance, lead-time, reminder and attendance-history dimensions.
Decision Required	Establish the permissible interpretation of these findings.
Options & Trade-off	Descriptive interpretation: supported by current evidence. Causal interpretation: requires evidence not presently established.
Rationale	Current analysis demonstrates patterns/associations, not causal relationships.
Current Position	Conditionally Approved: findings may inform project reasoning only within the demonstrated analytical scope.

DEC-006 — Analytical Interpretation Boundary (Analytical Governance)	
Consequence / Dependency	Controls overstatement in downstream interpretation and decision-making.
Verification / Closure	Review downstream outputs for descriptive, non-causal treatment.
Control References	TA-005; R-003
Status	Conditionally Approved

DEC-007 — Model Generalisation Limitation (Model Governance)	
Date / Required By	TBC / Before model acceptance
Owner / Authority	DS / PM
Impacted Tracks	DS, ML, PM
Decision Driver / Evidence	5-fold ROC-AUC = 0.6771 ± 0.0090 ; train/test ROC-AUC gap = 0.0571; segment-level performance limitations identified.
Decision Required	Determine the acceptance and monitoring treatment for the observed limitation.
Options & Trade-off	Conditional acceptance with controls: allows progression while retaining limitation. Defer acceptance: requires stronger evidence before progression.
Rationale	Evidence supports continued evaluation but requires the limitation to remain visible in acceptance.
Current Position	Pending formal disposition.
Consequence / Dependency	Affects model acceptance and monitoring treatment.
Verification / Closure	Document limitation, materiality and resulting control/acceptance position.
Control References	IIL-012–IIL-013; TA-008–TA-009; TA-017; R-004
Status	Pending Decision

DEC-008 — Technical vs Overall Readiness (Acceptance Governance)	
Date / Required By	Week 7 / Week 8 gate
Owner / Authority	PM / ML
Impacted Tracks	ML, PM, Integrated Solution

DEC-008 — Technical vs Overall Readiness (Acceptance Governance)	
Decision Driver / Evidence	69/69 automated tests passed; 948/948 batch scores completed; reproducibility, negative testing, regression correction and backtesting demonstrated. Operational integration remains incomplete.
Decision Required	Determine whether technical component readiness is reported separately from overall solution readiness.
Options & Trade-off	Separate states: accurately reflects evidence. Single state: simpler but risks overstating readiness.
Rationale	Component-level technical evidence and solution-level operational acceptance are materially different conditions.
Current Position	Conditionally Approved: ML technical readiness may be reported independently; it does not establish overall solution readiness.
Consequence / Dependency	Prevents technical test success being interpreted as integrated solution acceptance.
Verification / Closure	Maintain separate technical and overall readiness positions through the Week 8 gate.
Control References	IIL-014; TA-012–TA-018; R-005
Status	Conditionally Approved

DEC-009 — Blocked GenAI Scenarios (Test Governance)	
Date / Required By	TBC / Before final validation
Owner / Authority	GenAI / PM
Impacted Tracks	GenAI, PM
Decision Driver / Evidence	Two planned scenarios were not executed because Gemini returned 503/high-demand responses.
Decision Required	Determine the correct evidence status for blocked scenarios.
Options & Trade-off	Record as blocked/unexecuted: preserves evidence integrity. Treat as pass/fail: creates unsupported evidence.
Rationale	Service unavailability establishes inability to execute, not scenario success or failure.
Current Position	Conditionally Approved: scenarios remain unresolved coverage.
Consequence / Dependency	Prevents unsupported test status from entering readiness evidence. Depends on service availability.
Verification / Closure	Re-execute and disposition the scenarios when execution is possible.
Control References	IIL-008; TA-026; R-006

DEC-009 — Blocked GenAI Scenarios (Test Governance)	
Status	Conditionally Approved

DEC-010 — GenAI Safety & Validation Coverage (AI Governance)	
Date / Required By	TBC / Before E2E
Owner / Authority	PM / GenAI
Impacted Tracks	GenAI, PM, Integrated Solution
Decision Driver / Evidence	Scheduling urgency, emergency escalation, diagnosis, treatment/medication and KB-grounding boundaries have been tested to varying degrees; indirect emergency and privacy-sensitive scenarios remain incomplete.
Decision Required	Determine whether outstanding safety/privacy scenarios are mandatory before E2E acceptance.
Options & Trade-off	Proceed conditionally: faster progression with defined evidence gaps. Complete coverage first: stronger assurance before E2E.
Rationale	Existing evidence demonstrates selected boundaries but does not establish complete coverage of outstanding scenarios.
Current Position	Pending final coverage requirement and disposition.
Consequence / Dependency	Directly affects GenAI inclusion in broader validation.
Verification / Closure	Complete required scenarios and record disposition before E2E acceptance.
Control References	IIL-010–IIL-011; TA-022–TA-028; R-007
Status	Pending Decision

DEC-011 — Cross-Track Acceptance Standard (Integration Governance)	
Date / Required By	Week 7
Owner / Authority	PM / Track Owners
Impacted Tracks	Analytics, DS, ML, GenAI, PM
Decision Driver / Evidence	Workstream outputs exist, while some receiving-track validation, use or disposition remains outstanding.
Decision Required	Establish the acceptance condition for cross-track handoffs.


DEC-011 — Cross-Track Acceptance Standard (Integration Governance)	
Options & Trade-off	Activity-based: completion by originating track. Interface-based: receipt, validation and demonstrated downstream use/change.
Rationale	HealthConnect integration is dependent on functioning interfaces, not parallel completion alone.
Current Position	Conditionally Approved: downstream acceptance requires evidence of receipt, validation and integration/disposition.
Consequence / Dependency	Applies to unresolved Analytics→DS and DS→ML acceptance conditions.
Verification / Closure	Record receiving-track acceptance, integration result or formal disposition.
Control References	IIL-001; IIL-007; IIL-015; TA-006; TA-019; R-008
Status	Conditionally Approved

DEC-012 — E2E Validation Entry Condition (Validation Governance)	
Date / Required By	TBC / Before Week 8 integration
Owner / Authority	PM / All Track Owners
Impacted Tracks	All Tracks, Integrated Solution
Decision Driver / Evidence	Component testing is substantial, but complete HealthConnect workflow validation has not been demonstrated.
Decision Required	Establish when E2E validation can be treated as valid project evidence.
Options & Trade-off	Execute before critical dependencies clear: incomplete evidence. Clear critical interfaces first: stronger assurance with additional dependency management.
Rationale	E2E evidence has limited value while critical upstream interfaces remain uncontrolled.
Current Position	Conditionally Approved: clear critical DS→ML, threshold and decision/intervention conditions before final E2E validation.
Consequence / Dependency	Controls the validity of the final integrated test.
Verification / Closure	Execute E2E scenarios and disposition material findings.
Control References	DEC-001–DEC-004; IIL-015; TA-020; TA-029; R-009
Status	Conditionally Approved

DEC-013 — Week 8 Readiness Position (Gate / Readiness)	
Date / Required By	TBC / Week 8 gate
Owner / Authority	PM / Programme Governance
Impacted Tracks	All Tracks
Decision Driver / Evidence	Critical integration, operationalisation and E2E conditions remain unresolved; workstream completion alone does not establish readiness.
Decision Required	Determine whether defined Week 8 entry conditions have been satisfied.
Options & Trade-off	Enter with formally accepted conditions; requires controlled residual items. Defer: requires critical conditions to be cleared first.
Rationale	Final integration/presentation should rely on demonstrated acceptance and dispositioned exceptions rather than activity completion.
Current Position	Pending completion of critical actions and formal readiness assessment.
Consequence / Dependency	Controls premature progression into final integration/presentation.
Verification / Closure	Approved Week 8 readiness assessment and gate position; critical issue/risk disposition and E2E evidence.
Control References	IIL-017; TA-034; R-001; R-002; R-007; R-009
Status	Pending Decision

4. DECISION DEPENDENCY STRUCTURE

The material decision dependencies currently converge on the following control path:

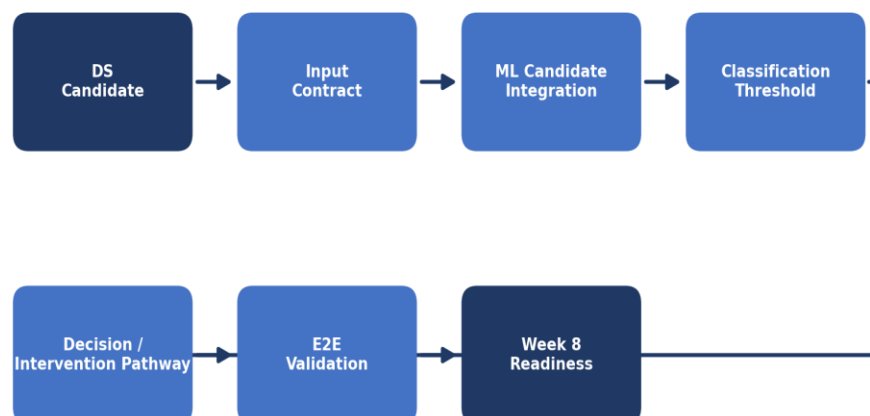

Supporting decisions govern the evidence entering that path:

- Analytics evidence acceptance and interpretation establish the conditions under which analytical findings may support downstream work.
- Model generalisation treatment establishes how known performance limitations affect acceptance.
- Technical versus overall readiness prevents component-level evidence from being conflated with solution readiness.
- GenAI coverage decisions determine whether outstanding safety and validation gaps can be carried into final integration.
- Cross-track acceptance establishes the common rule for receiving-track validation.

These relationships identify decision dependencies, not a rigid activity sequence.

5. DECISION QUALITY & CLOSURE CRITERIA

A material decision is considered controlled only when the record establishes:

Control	Requirement
Evidence	The evidence giving rise to the decision is identifiable.
Decision Requirement	The precise decision question is stated.
Authority	The appropriate decision owner/authority is identified.
Options / Trade-off	Material alternatives and consequences are understood where applicable.
Rationale	The position is defensible against the available evidence.
Impact	Downstream project or operational consequences are identified.
Dependencies	Conditions required for implementation or closure are explicit.
Verification	Objective evidence required to confirm implementation is defined.
Residual Condition	Remaining limitations are recorded rather than implicitly closed.

6. ESCALATION & EXCEPTION CONTROL

Escalation is required where a decision:


- Blocks a critical integration dependency;
- Affects a safety or privacy boundary;
- Creates unresolved acceptance conflict between tracks;
- Changes the controlled model, input contract, threshold, decision logic or intervention pathway;
- Materially threatens a project gate or Week 8 entry condition;
- Requires authority beyond the originating track;
- Cannot be resolved because required evidence or an external execution dependency is unavailable; or

- Leaves a material residual condition without an accepted treatment.

Escalation Record



Escalation Route



Where an unresolved decision creates project exposure or an active interface blocker, its status must remain aligned with the Risk & Dependency Register and/or Integration & Issue Log.

7. DECISION GOVERNANCE CROSS-REFERENCE

Artifact	Control Function	Decision Log Relationship
Testing Activity Tracker	Test execution, findings, retesting and disposition.	Provides decision evidence.


Artifact	Control Function	Decision Log Relationship
Integration & Issue Log	Interface issues, blockers and resolution.	Identifies conditions requiring decision or acceptance.
Risk & Dependency Register	Project exposure and dependency treatment.	Captures consequences arising from unresolved decisions.
Updated Timeline	Schedule and dependency control.	Reflects material decision-driven changes.
Decision Log	Decision requirement, authority, rationale, position and verification.	Central decision-control record.
Week 8 Readiness Assessment	Formal readiness determination.	Consumes outstanding decision status and evidence.

8. WEEK 7 DECISION POSITION

The Week 7 evidence base has established several controlled positions, including:

- analytical findings remain within a descriptive/associational interpretation boundary;
- ML technical validation is distinguishable from overall solution readiness;
- blocked GenAI executions must remain blocked/unexecuted rather than being assigned an unsupported result; and
- cross-track completion requires receiving-track validation or formal disposition, not originating-track completion alone.

The material decisions still requiring resolution concern:

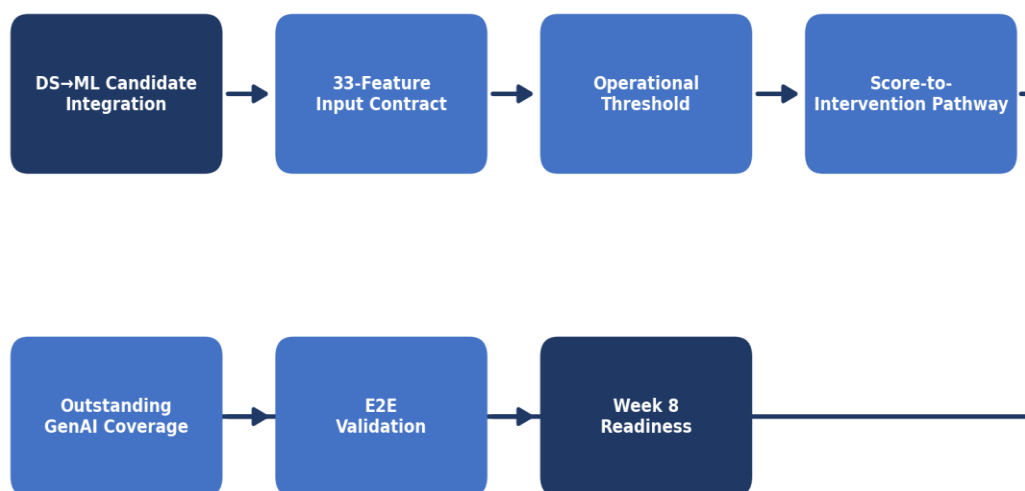

The project therefore has a defined decision-control path into Week 8, but the final readiness position remains pending evidence-based gate assessment.

Governing Control Principle

A decision is not controlled by recording a position alone; it is controlled when the evidence, authority, consequence, dependency and verification path are explicit and traceable.
