

ANALYSTLAB AFRICA
EXPERIENCE LAB INTERNSHIP PROGRAMME
HEALTHCONNECT CLINIC EXPERIENCE LAB
OUTSTANDING ACTIONS & WEEK 8 INTEGRATION ACTION REGISTER


Improving Patient Appointment Attendance and Healthcare Support Using Data and AI

Field	Detail
Project:	Improving Patient Appointment Attendance and Healthcare Support Using Data and AI
Programme:	AnalystLab Africa Experience Lab
Workstream:	Project Management
Reporting Period:	Week 7
Document Type:	Outstanding Actions & Week 8 Integration Action Register
Version:	1.0
Register Owner:	Project Management
Status:	AMBER-RED — CONTROLLED WITH MATERIAL INTEGRATION ACTIONS OUTSTANDING

1. REGISTER PURPOSE

This register is the forward-control mechanism for converting unresolved Week 7 conditions into verified Week 8 outcomes.

It identifies the actions required to remove material testing, integration, acceptance and readiness constraints established during Week 7 and provides a controlled basis for tracking each action through:

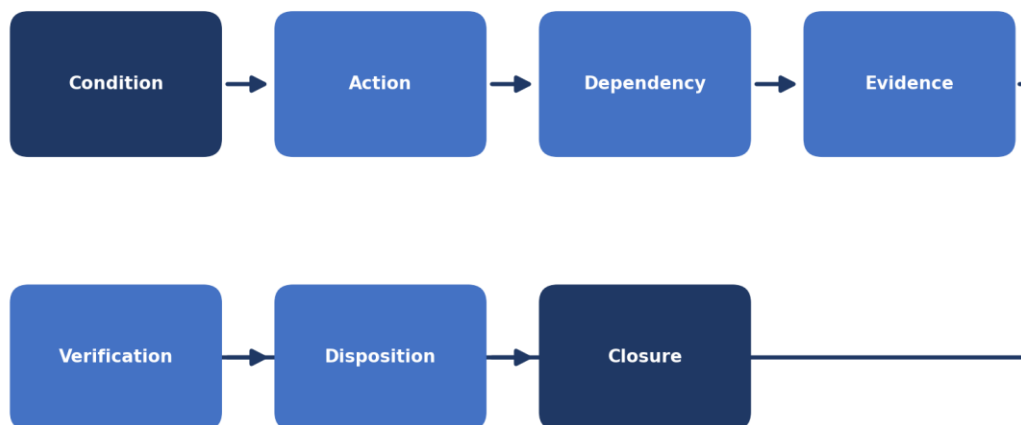

The register deliberately does not reproduce the detailed content of the Risk & Dependency Register, Integration & Issue Log, Testing Activity Tracker, Decision Log, Cross-Track Coordination Record or Readiness Assessment. Those records remain the authoritative controls for their respective purposes.

This register instead answers one management question:

What must now be completed, by whom, against what dependency and evidence, before the affected condition can be considered closed or accepted?


2. CONTROL STANDARD

An action is not closed because an activity has been performed.


Closure requires evidence that:

- 1. The required action was executed;
- 2. The intended outcome was achieved;
- 3. The outcome was verified against the applicable requirement or acceptance basis;
- 4. Any affected receiving workstream has been able to use or validate the output where an interface is involved;
- 5. Material residual limitations have been documented and dispositioned; and
- 6. The relevant source control has been updated.


For cross-track actions, the minimum closure path is:

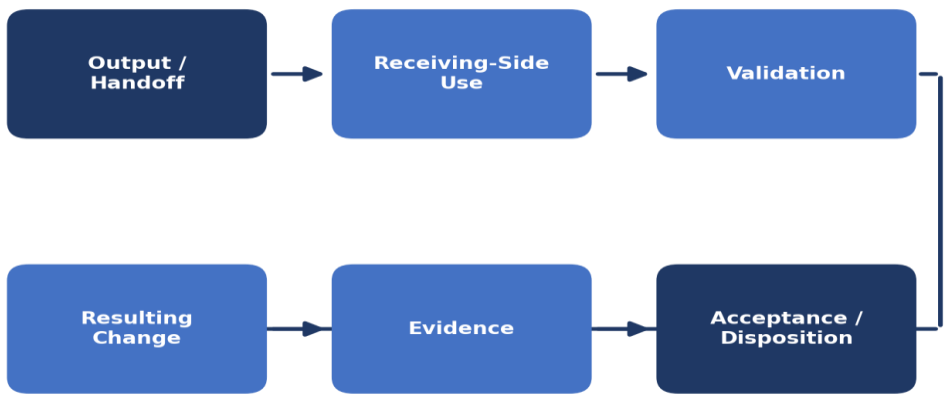

For testing actions:



For readiness actions:



3. ACTION CONTROL CLASSIFICATION

Class	Control Purpose	Closure Requirement
Critical Integration	Removes a dependency preventing a material interface from being validated.	Interface demonstrated and receiving-side condition verified.
Critical Validation	Establishes evidence that a material component or workflow performs as required.	Test/re-test evidence and documented disposition.
Acceptance	Converts available evidence into a formally accepted or conditionally accepted position.	Receiving/management acceptance recorded.
Controlled Continuation	Completes validation that can proceed without independently preventing controlled Week 8 progression.	Required validation completed and findings dispositioned.
Governance	Maintains consistency across PM control records and readiness decisions.	Records reconciled and traceability maintained.

4. STATUS DEFINITIONS

Status	Definition
Open	Action is approved/required but execution has not commenced or remains outstanding.
In Progress	Execution is underway and closure requirements remain outstanding.
Pending Validation	Action/output has been completed to the point of requiring verification or receiving-side confirmation.
Blocked	A prerequisite or external constraint prevents execution.
Conditionally Complete	Core action is complete but a defined residual condition remains under control.
Closed	Outcome has been evidenced, verified and formally dispositioned with no further action under scope.
Accepted Residual	Remaining limitation has been explicitly documented and accepted as a controlled residual condition.

5. MASTER ACTION REGISTER

Each action record below captures the outstanding condition, required action, ownership, dependency, evidence requirement, class, status, closure criterion and escalation trigger.

WA-01 (CTC-01 / CTV-001 / REC-09)	
Outstanding Condition	Analytical findings are available, but their downstream disposition within the modelling workflow is not fully evidenced.
Required Action	Review the relevant analytical findings and formally document which findings/features are incorporated, excluded or retained for further validation.
Accountable Owner	Data Science
Supporting Track	Data Analytics
Dependency	Validated analytical evidence
Required Evidence	Receiving-side review/disposition; resulting model/data change where applicable
Target Checkpoint	Week 8 Integration
Class	Critical Integration
Status	Open
Closure / Acceptance Criterion	DS disposition is documented and traceable to the analytical evidence.
Escalation Trigger	No receiving-side disposition before integration checkpoint.

WA-02 (IIL-001 / CTC-02 / REC-01)	
Outstanding Condition	The actual DS-selected model candidate has not been evidenced as transferred to ML.
Required Action	Execute the controlled handoff of the final selected DS candidate and obtain receiving-side confirmation from ML.
Accountable Owner	Data Science
Supporting Track	ML Engineering
Dependency	Final candidate selection
Required Evidence	Candidate package/version; handoff record; ML acknowledgement
Target Checkpoint	Week 8 Integration
Class	Critical Integration
Status	Open
Closure / Acceptance Criterion	Actual selected candidate is demonstrably received by ML.

WA-02 (IIL-001 / CTC-02 / REC-01)	
Escalation Trigger	Candidate remains untransferred at integration checkpoint.

WA-03 (IIL-002 / CTV-005 / REC-02)	
Outstanding Condition	Compatibility between the DS 33-feature structure and ML preprocessing/input requirements remains unverified.
Required Action	Reconcile feature names/structure, preprocessing assumptions and required model inputs between DS and ML.
Accountable Owner	Data Science / ML Engineering
Supporting Track	Project Management
Dependency	WA-02
Required Evidence	Feature/schema mapping; preprocessing reconciliation; receiving-side confirmation
Target Checkpoint	Before Candidate Execution
Class	Critical Integration
Status	Open
Closure / Acceptance Criterion	A jointly verified input/preprocessing contract exists.
Escalation Trigger	Any unresolved mismatch capable of invalidating candidate execution.

WA-04 (IIL-001 / CTV-004 / REC-03)	
Outstanding Condition	ML technical capability has been demonstrated using a stand-in RF, but the actual DS-selected candidate has not been executed through the validated pipeline.
Required Action	Execute the actual DS candidate through the ML pipeline and verify the resulting scoring behaviour and output structure.
Accountable Owner	ML Engineering
Supporting Track	Data Science
Dependency	WA-02, WA-03
Required Evidence	Execution record; scoring output; probability validity; test evidence
Target Checkpoint	Week 8 Model Integration
Class	Critical Validation

WA-04 (IIL-001 / CTV-004 / REC-03)	
Status	Open
Closure / Acceptance Criterion	Actual candidate executes successfully with expected outputs and no unresolved material interface defect.
Escalation Trigger	Candidate execution fails, produces incompatible outputs or exposes unresolved preprocessing defects.

WA-05 (DEC-003 / IIL-003 / REC-05)	
Outstanding Condition	A candidate classification threshold has been considered, but no final operational threshold has been formally accepted.
Required Action	Review model evidence and operational trade-offs and record the threshold decision for the intended use case.
Accountable Owner	Data Science / Project Management
Supporting Track	ML Engineering
Dependency	WA-04
Required Evidence	Threshold analysis; selected threshold; decision rationale; decision record
Target Checkpoint	Before Decision Validation
Class	Acceptance
Status	Open
Closure / Acceptance Criterion	Threshold is formally dispositioned and linked to the validated candidate evidence.
Escalation Trigger	Threshold remains unresolved when score-to-decision validation is due.

WA-06 (IIL-004 / CTV-008 / REC-06)	
Outstanding Condition	Valid probability outputs exist, but the transition from model score to an accepted decision rule has not been demonstrated.
Required Action	Define and test the score-to-decision rule using the accepted threshold and validated model output.
Accountable Owner	ML Engineering / Project Management
Supporting Track	Data Science
Dependency	WA-05

WA-06 (IIL-004 / CTV-008 / REC-06)	
Required Evidence	Decision-rule test; expected/actual result; acceptance evidence
Target Checkpoint	Week 8 Decision Validation
Class	Critical Validation
Status	Open
Closure / Acceptance Criterion	Score-to-decision behaviour is demonstrated and accepted.
Escalation Trigger	Decision output cannot be reproduced or does not align with the accepted threshold.

WA-07 (IIL-004 / CTV-009 / REC-07)	
Outstanding Condition	The downstream intervention pathway has not been demonstrated from an accepted decision output.
Required Action	Validate how the resulting decision translates into the intended HealthConnect intervention/action pathway.
Accountable Owner	Project Management
Supporting Track	ML Engineering / Data Analytics
Dependency	WA-06
Required Evidence	Workflow/scenario record; resulting action; validation evidence
Target Checkpoint	Week 8 E2E Preparation
Class	Critical Validation
Status	Open
Closure / Acceptance Criterion	Decision-to-intervention pathway is demonstrated and dispositioned.
Escalation Trigger	Intervention pathway remains undefined or untestable.

WA-08 (IIL-005 / CTV-002 / REC-08)	
Outstanding Condition	Dashboard KPI values and definitions require final reconciliation before analytical evidence is formally accepted.
Required Action	Reconcile dashboard KPIs against the approved analytical dataset and confirm definitions and displayed values.
Accountable Owner	Data Analytics

WA-08 (IIL-005 / CTV-002 / REC-08)	
Supporting Track	Project Management
Dependency	Validated analytical dataset
Required Evidence	KPI reconciliation record; final definitions; discrepancy disposition
Target Checkpoint	Week 8 Integration
Class	Acceptance
Status	Pending Validation
Closure / Acceptance Criterion	Material KPI discrepancies are resolved or formally dispositioned and acceptance is recorded.
Escalation Trigger	Material discrepancy remains unresolved at acceptance checkpoint.

WA-09 (IIL-006 / CTV-003)	
Outstanding Condition	Runtime behaviour of dashboard filters and segmented views remains incompletely evidenced.
Required Action	Execute representative filter and segmentation checks and verify consistency of displayed outputs.
Accountable Owner	Data Analytics
Supporting Track	Project Management
Dependency	Dashboard availability
Required Evidence	Test records; output evidence; findings/disposition
Target Checkpoint	Week 8 Integration
Class	Controlled Continuation
Status	Pending Validation
Closure / Acceptance Criterion	Required interactions are tested and material defects are dispositioned.
Escalation Trigger	Material interaction defect affects interpretation of reported evidence.

WA-10 (IIL-008 / CTV-016 / REC-10)	
Outstanding Condition	Two planned GenAI scenarios could not be executed because of Gemini service unavailability.
Required Action	Re-run the blocked scenarios when the validation environment becomes available and record actual outcomes.
Accountable Owner	Generative AI
Supporting Track	Project Management

WA-10 (IIL-008 / CTV-016 / REC-10)	
Dependency	Validation environment/service availability
Required Evidence	Scenario execution evidence; expected-vs-actual assessment; disposition
Target Checkpoint	GenAI Validation Checkpoint
Class	Critical Validation
Status	Blocked
Closure / Acceptance Criterion	Both scenarios have been executed and formally dispositioned.
Escalation Trigger	Service remains unavailable at the required validation checkpoint.

WA-11 (IIL-009 / IIL-010 / IIL-011 / REC-11–13)	
Outstanding Condition	Broader GenAI consistency, indirect/vague emergency phrasing and privacy-sensitive boundary coverage remain incomplete.
Required Action	Execute the outstanding scenarios against the approved response boundaries and document all findings and required refinements.
Accountable Owner	Generative AI
Supporting Track	Project Management
Dependency	WA-10 / validation environment
Required Evidence	Scenario matrix; response evidence; refinement/re-test records; disposition
Target Checkpoint	GenAI Validation Checkpoint
Class	Critical Validation
Status	Open
Closure / Acceptance Criterion	Material safety, consistency and privacy-sensitive scenarios have documented outcomes and dispositions.
Escalation Trigger	Material boundary remains untested before final acceptance.

WA-12 (IIL-015 / CTV-018 / REC-16)	
Outstanding Condition	Full HealthConnect end-to-end behaviour has not yet been demonstrated across the relevant interfaces.

WA-12 (IIL-015 / CTV-018 / REC-16)	
Required Action	Execute an integrated scenario covering the applicable analytical/model, decision/intervention and support workflow components.
Accountable Owner	Project Management
Supporting Track	All Relevant Tracks
Dependency	WA-04–WA-11
Required Evidence	E2E scenario record; interface outputs; findings; acceptance/disposition
Target Checkpoint	Week 8 E2E Validation
Class	Critical Integration
Status	Pending
Closure / Acceptance Criterion	Material interfaces demonstrate expected behaviour and the E2E result is formally dispositioned.
Escalation Trigger	Critical interface remains unverified or produces an unresolved material defect.

WA-13 (DEC-007 / REC-15)	
Outstanding Condition	Model performance evidence exists, but the final acceptance position remains dependent on actual candidate integration and operational interpretation.
Required Action	Consolidate validated candidate performance, robustness evidence, known limitations and threshold implications into the final model acceptance position.
Accountable Owner	Data Science
Supporting Track	ML Engineering / Project Management
Dependency	WA-04, WA-05
Required Evidence	Final performance evidence; limitation statement; acceptance record
Target Checkpoint	Week 8 Model Acceptance
Class	Acceptance
Status	Pending
Closure / Acceptance Criterion	Model acceptance position is formally recorded with limitations and evidence.
Escalation Trigger	Acceptance cannot be established from the integrated candidate evidence.

WA-14 (DEC-010 / REC-10–13)	
Outstanding Condition	GenAI validation evidence remains conditional because blocked and untested scenarios have not all been dispositioned.
Required Action	Reconcile executed, blocked and not-run scenarios and update the formal GenAI validation position.
Accountable Owner	Generative AI / Project Management
Supporting Track	—
Dependency	WA-10, WA-11
Required Evidence	Updated scenario status; validation summary; disposition record
Target Checkpoint	GenAI Acceptance Checkpoint
Class	Acceptance
Status	In Progress
Closure / Acceptance Criterion	No material outstanding scenario remains without a documented disposition.
Escalation Trigger	Safety/privacy/consistency gap remains unaddressed at acceptance checkpoint.

WA-15 (DEC-011 / CTV-001–018 / CTC-11)	
Outstanding Condition	Critical interfaces do not yet have complete receiving-side acceptance evidence.
Required Action	Obtain and record receiving-side acceptance, conditional acceptance, pending validation or controlled residual disposition for each material interface.
Accountable Owner	Project Management
Supporting Track	All Workstreams
Dependency	WA-01–WA-14
Required Evidence	Updated Cross-Track Validation & Acceptance Matrix
Target Checkpoint	Week 8 Integration Gate
Class	Critical Integration
Status	Open
Closure / Acceptance Criterion	Every critical interface has an explicit and evidence-backed disposition.
Escalation Trigger	Critical interface remains without a controlled disposition.

WA-16 (IIL-016 / R-001-R-009 / DEC-013)	
Outstanding Condition	Week 7 findings require final reconciliation across the PM control set before the next readiness determination.
Required Action	Reconcile outstanding actions with risks, issues, dependencies, decisions, schedule and readiness position; update affected records consistently.
Accountable Owner	Project Management
Supporting Track	All Workstreams
Dependency	Material action updates
Required Evidence	Updated control records; reconciliation check
Target Checkpoint	Week 8 Readiness Gate
Class	Governance
Status	In Progress
Closure / Acceptance Criterion	All material open conditions have consistent status and traceability across the control set.
Escalation Trigger	Material contradiction, untracked dependency or stale readiness position remains.

6. ACTION DEPENDENCY STRUCTURE

The material Week 8 action path is dependency-driven rather than activity-driven.

Primary Integration Chain



Parallel Validation Stream



GenAI service recovery and outstanding scenario validation proceed in parallel with the core model-integration sequence, but unresolved material safety, consistency or privacy-sensitive conditions remain relevant to overall acceptance.

7. WEEK 8 ACTION GATES

Gate	Required Action Position	Minimum Exit Evidence	Current Position
G-A — Candidate Integration	WA-02–WA-04	Actual DS candidate received, schema reconciled and executed through ML	Not Cleared
G-B — Model Acceptance	WA-05, WA-13	Threshold and integrated candidate acceptance position documented	Not Cleared
G-C — Operational Logic	WA-06–WA-07	Score-to-decision and decision-to-intervention pathways validated	Not Cleared
G-D — Analytical Acceptance	WA-01, WA-08, WA-09	Analytical evidence and dashboard outputs reconciled/dispositioned	Not Cleared
G-E — GenAI Validation	WA-10, WA-11, WA-14	Outstanding scenarios executed or formally dispositioned	Not Cleared
G-F — Cross-Track Acceptance	WA-15	Critical interfaces have explicit receiving-side disposition	Not Cleared
G-G — E2E Validation	WA-12	Integrated HealthConnect scenario demonstrated and dispositioned	Not Cleared
G-H — Readiness Control	WA-16	PM control records reconciled and readiness position updated	Not Cleared

These gates are control checkpoints, not additional project milestones. Their purpose is to prevent progression from being treated as complete where prerequisite evidence remains outstanding.

8. ESCALATION CONTROL

An action shall be escalated when one or more of the following conditions occurs:

- A Critical Integration action remains blocked at its required checkpoint;
- A dependency prevents a downstream action from commencing;
- The actual DS candidate differs from the candidate used in prior technical evidence without documented reconciliation;
- Schema or preprocessing incompatibility threatens validity of candidate execution;
- The score-to-decision or decision-to-intervention pathway cannot be demonstrated;

- A material GenAI safety, privacy-sensitive or consistency condition remains untested;
- An external service dependency prevents required validation;
- An unresolved finding materially changes the established readiness position;
- PM control records contain materially inconsistent status, ownership or disposition;
- An action remains open beyond the relevant Week 8 gate without an approved controlled disposition.

Escalation shall result in an updated impact, dependency, owner, action and expected resolution position rather than merely a status change.

9. CLOSURE AND DISPOSITION RULES

9.1 Closed

Use Closed only where:

- The required action has been completed;
- The intended outcome has been demonstrated;
- Verification evidence is available;
- Relevant downstream use or acceptance has been established where applicable; and
- No material residual condition remains within scope.

9.2 Conditionally Complete

Use Conditionally Complete where the principal action has been achieved but a clearly defined, non-blocking residual activity remains under active control.

9.3 Accepted Residual

Use Accepted Residual only where the remaining limitation is explicitly documented, its effect is understood, and the responsible control authority has accepted continuation with that limitation.

9.4 Blocked

Use Blocked where execution cannot reasonably proceed because a prerequisite or external dependency is unavailable.

A blocked action must retain its blocking dependency and recovery condition; it should not be converted to Closed merely because the required activity was attempted.

10. ACCOUNTABILITY MODEL

The accountable owner is responsible for driving the action through to verified disposition. Supporting tracks provide the technical or operational input required for completion.

Action Domain	Accountable Role
Analytics evidence / dashboard acceptance	Data Analytics
Analytics → DS disposition	Data Science
Candidate transfer / model interface	Data Science + ML Engineering

Action Domain	Accountable Role
Model execution / technical scoring	ML Engineering
Threshold and model acceptance	Data Science + Project Management
Decision / intervention pathway	Project Management
GenAI validation and boundary testing	Generative AI
Cross-track acceptance	Project Management
E2E validation coordination	Project Management
Risk / issue / decision / schedule reconciliation	Project Management

Accountability indicates ownership of closure control, not sole responsibility for performing every underlying technical task.

11. CONTROL-RECORD INTERFACE

This register operates as the action layer across the existing PM control framework:

Control Record	Primary Question
Testing Activity Tracker	What was tested and what was the result?
Integration & Issue Log	What material integration condition exists?
Risk & Dependency Register	What potential exposure or dependency requires control?
Decision Log	What requires or has received a formal decision?
Cross-Track Coordination Record	What was exchanged, acted upon and followed up?
Cross-Track Validation & Acceptance Matrix	Was the interface/output actually validated and accepted?
Project Timeline & Schedule Control	Where does the action sit in the delivery sequence?
Testing Progress & Status Report	What is the consolidated testing position?
Week 7–8 Readiness Assessment	What is the resulting readiness position?
This Register	What must happen next to remove or disposition the outstanding condition?

This separation prevents the action register from becoming a duplicate issue or risk register while preserving traceability to the governing records.

12. WEEK 7 → WEEK 8 ACTION POSITION

The Week 7 evidence base demonstrates meaningful progress in component testing, technical refinement and PM control. The remaining work is concentrated principally at the interfaces between validated components and their operational use.

The outstanding action profile is therefore characterised by:

- Incomplete DS → ML candidate transfer;
- Unresolved 33-feature/preprocessing reconciliation;
- Pending execution of the actual DS candidate through ML;
- Threshold and operational decision acceptance not yet completed;
- Decision-to-intervention behaviour not yet demonstrated;
- Outstanding analytical acceptance checks;
- Incomplete GenAI scenario coverage, including blocked validation;
- Incomplete receiving-side cross-track acceptance;
- Absence of full HealthConnect end-to-end validation.

The control implication is material:

The principal Week 8 requirement is not additional parallel activity; it is conversion of existing workstream outputs into verified, usable and accepted cross-track outcomes.

13. CURRENT MANAGEMENT DETERMINATION

ACTION-CONTROL POSITION: AMBER-RED


The Week 7 outstanding-action profile is sufficiently defined to support controlled Week 8 progression. However, the critical integration sequence remains open and several actions are directly prerequisite to final solution acceptance. Accordingly:

WEEK 8 MAY PROCEED UNDER CONTROLLED INTEGRATION CONDITIONS.

However:

NO ACTION SHALL BE TREATED AS CLOSED ON THE BASIS OF ACTIVITY COMPLETION ALONE, AND THE SOLUTION SHALL NOT BE REPRESENTED AS FINALLY INTEGRATED OR OPERATIONALLY ACCEPTED UNTIL THE RELEVANT CRITICAL ACTIONS HAVE BEEN EVIDENCED, VERIFIED AND DISPOSITIONED.

The immediate management focus is therefore:

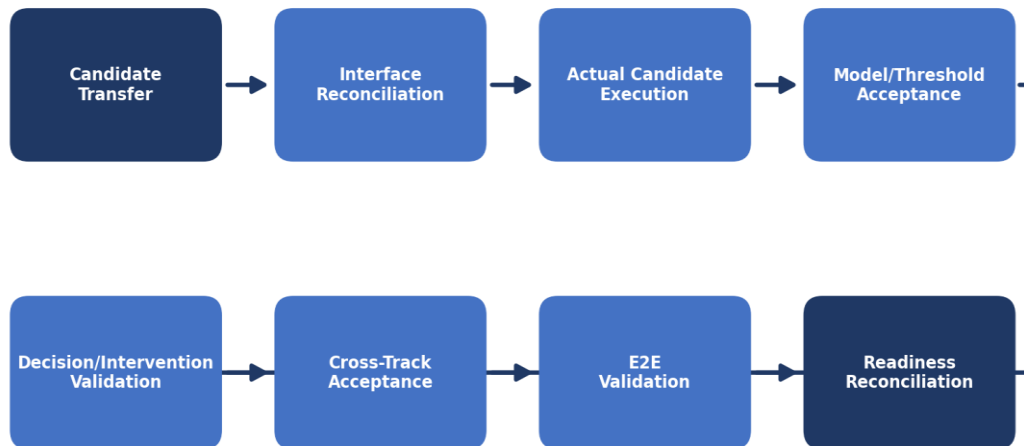

14. REGISTER GOVERNANCE

The register shall be reviewed at each Week 8 integration control point and updated whenever:

- An action changes status;
- A dependency is cleared or newly identified;
- Evidence is received;
- A blocked action becomes executable;
- An acceptance decision is made;
- A residual limitation is accepted;
- A material finding changes the action requirement;
- An action is closed;
- The resulting readiness position changes.

Where an action is closed, the closure evidence shall also be reflected in the originating control record to preserve a consistent project audit trail.

15. VERSION CONTROL

Version	Reporting Period	Change	Status
V1.0	Week 7	Initial controlled register establishing outstanding Week 7 actions and Week 8 integration closure requirements.	Current

Next Update Trigger: Material action status change, evidence receipt, dependency resolution or readiness reassessment
