

HEALTHCONNECT CLINIC EXPERIENCE LAB

WEEK 7 — UPDATED PROJECT TIMELINE & SCHEDULE CONTROL

Improving Patient Appointment Attendance and Healthcare Support Using Data and AI

Document Control

Field	Detail
Project	Improving Patient Appointment Attendance and Healthcare Support Using Data and AI
Programme	AnalystLab Africa Experience Lab
Document Type	Updated Project Timeline & Schedule Control
Reporting Period	Week 7
Version	4.0
Baseline Reference	High-Level Timeline V1.0 / Execution Timeline V2.0 / Week 6 Controlled Timeline V3.0
Schedule Owner	Project Management
Schedule Status	AMBER-RED — Controlled with Material Integration Dependencies

1. DOCUMENT PURPOSE

This document establishes the controlled project schedule position for the HealthConnect Clinic Experience Lab at the end of Week 7.

It updates the approved delivery baseline using the latest evidence from testing, refinement, retesting, cross-track validation and dependency review.

The timeline governs:

- Project delivery sequence;
- Activity and workstream dependencies;
- Milestone progression;

- Stage-gate movement;
- Schedule-driving conditions;
- Testing-to-integration sequencing;
- Forward delivery requirements;
- Schedule constraints and exposures;
- schedule variance control; and
- Conditions for progression into Week 8.

This document does not replace the detailed Testing Activity Tracker, Integration & Issue Log, Risk & Dependency Register, Decision Log or Week 8 Readiness Assessment. Those records retain their respective control purposes.

2. SCHEDULE CONTROL FRAMEWORK

The project continues to operate under the approved dependency-driven scheduling model.

Control Element	Controlled Position
Scheduling Method	Dependency-driven
Delivery Model	Controlled parallel workstreams
Schedule Authority	Approved M01–M12 milestone architecture
Gate Framework	G1–G12
Detailed Schedule Basis	WBS activities and logical predecessor/successor relationships
Current Control Phase	Testing, refinement, retesting and cross-track validation
Forward Phase	Final integration, E2E validation and readiness determination
Schedule Owner	Project Management
Progression Principle	Dependent work progresses when its required predecessor evidence is available and accepted
Baseline Protection	Historical schedule positions are not retrospectively altered without controlled change

The schedule permits workstreams to progress concurrently where their activities do not require unresolved upstream conditions.

Where a dependency is material to a successor activity, the successor remains controlled by that dependency irrespective of whether independent work elsewhere has progressed.

3. WEEK 7 SCHEDULE UPDATE BASIS

Version 4.0 reflects the change in project control position established during Week 7. The update is based on:

- Availability of the Power BI analytical dashboard and supporting analytical evidence;
- Completion of substantive Data Science validation and refinement activity;
- Establishment of the refined 33-feature Random Forest candidate;
- ML component, interface, regression, robustness, reproducibility and batch-scoring evidence;
- Distinction between ML technical validation and overall solution acceptance;
- GenAI scenario testing, refinement and retesting;
- External-service constraints affecting two planned GenAI scenarios;
- Identified receiving-side acceptance gaps;
- Outstanding DS→ML candidate transfer and input-contract reconciliation;
- Unresolved threshold and operational decision logic;
- Incomplete Analytics acceptance/disposition;
- Incomplete broader GenAI safety, consistency and privacy validation; and
- Absence of full HealthConnect end-to-end validation.

Schedule Implication

The project has moved beyond the principal Week 6 concern of development and integration preparation.

The controlling scheduling issue is now the conversion of workstream outputs into accepted, interoperable and validated downstream inputs.

4. DELIVERY ARCHITECTURE

The approved delivery architecture remains unchanged.

WBS	Delivery Area	Primary Output	Gate
1	Project Initiation & Governance	Project governance and control framework	G1
2	Problem & Requirements	Validated problem and requirements	G2
3	Data Foundation	Analysis-ready data foundation	G3

WBS	Delivery Area	Primary Output	Gate
4	Attendance Analytics	Attendance analysis and insights	G4
5	Predictive Intelligence	Evaluated no-show prediction capability	G5
6	Patient Engagement	Intervention model	G6
7	Generative AI Support	AI support capability and controls	G7
8	Operational Integration	Integrated future-state workflow	G8
9	Testing & Validation	Validated solution	G9
10	Implementation Readiness	Implementation-readiness assessment	G10
11	Monitoring & Evaluation	Measurement framework	G11
12	Closure & Recommendations	Final project assessment	G12

No change to the WBS architecture is introduced by this update.

5. CURRENT SCHEDULE POSITION

Schedule Horizon	Position at Week 7	Control Basis
Completed	Project baseline and problem-definition stages	G1 and G2 achieved
Established / Controlled	Data foundation and attendance analytics	Current evidence supports continued use; formal acceptance remains controlled
Advanced	Predictive development and ML technical validation	Candidate and technical evidence substantially developed
Conditional	GenAI support capability	Selected behaviours validated; coverage remains incomplete
Current	Cross-track testing and validation	Interfaces require receiving-side evidence and acceptance
Immediate Forward	Actual DS→ML integration and operationalisation	Dependent on candidate/interface conditions
Week 8	Final integration, E2E validation and readiness determination	Mandatory entry conditions apply
Downstream	Implementation readiness, measurement and closure	Dependent on validated and accepted solution

6. INTEGRATED FORWARD ACTIVITY SCHEDULE

The following register represents the current controlled forward schedule. It establishes the logical sequence without inventing unsupported calendar dates or duration estimates.

ID	Activity	Primary Owner	Position	Next Action
SCH-01	Reconcile analytical evidence and KPI definitions	Data Analytics	Open	Complete reconciliation
SCH-02	Confirm Analytics→DS downstream disposition	Data Analytics / Data Science	Open	Record receiving-side disposition
SCH-03	Confirm final DS candidate for integration	Data Science	Established	Controlled transfer
SCH-04	Reconcile 33-feature structure and preprocessing	Data Science / ML	Outstanding	Confirm input compatibility
SCH-05	Execute actual DS candidate through ML interface	ML / Data Science	Outstanding	Execute and record evidence
SCH-06	Validate candidate scoring and outputs	ML	Dependent	Verify output behaviour
SCH-07	Determine operational classification threshold	Data Science / PM	Pending acceptance	Record controlled decision
SCH-08	Validate score-to-decision logic	ML / PM	Not established	Define and test decision rule
SCH-09	Validate decision-to-intervention pathway	PM / Relevant Tracks	Not established	Execute workflow validation
SCH-10	Complete outstanding GenAI scenarios	GenAI	Partially blocked	Re-execute or formally disposition
SCH-11	Complete broader GenAI safety, consistency and privacy coverage	GenAI	Incomplete	Execute controlled scenarios
SCH-12	Complete cross-track receiving-side acceptance	Relevant Tracks / PM	Incomplete	Validate and record acceptance
SCH-13	Execute full HealthConnect E2E validation	All Tracks / PM	Not run	Execute after entry conditions
SCH-14	Reconcile issues, risks and decisions	PM	Ongoing	Update control baseline
SCH-15	Conduct Week 8 readiness assessment	PM	Pending	Determine progression position
SCH-16	Final integration and presentation preparation	All Tracks / PM	Downstream	Proceed under approved gate conditions

Schedule Sequencing Principle

SCH-01, SCH-02, SCH-10, SCH-11 and relevant PM control activities may progress in parallel where prerequisites permit.

SCH-05 through SCH-09 are materially dependent and should not be treated as independent completion activities.

SCH-13 remains downstream of the material interface conditions.

7. MATERIAL MILESTONE REGISTER

ID	Milestone	Week 7 Position	Status
M01	Project Baseline Established	Achieved	COMPLETE
M02	Problem Validated	Achieved	COMPLETE
M03	Data Foundation Ready	Current analytical work supported; formal readiness remains controlled	CONTROLLED
M04	Attendance Insights Established	Substantive findings available; acceptance/disposition incomplete	CONDITIONAL
M05	Prediction Capability Validated	Refined candidate established; integration and acceptance remain	CONDITIONAL
M06	Intervention Model Established	Dependent on accepted decision pathway	IN PROGRESS
M07	AI Support Capability Validated	Targeted evidence available; material coverage remains	CONDITIONAL
M08	Integrated Workflow Established	Full cross-track workflow not yet established	PENDING
M09	Solution Validated	Not established	PENDING
M10	Implementation Readiness Assessed	Downstream	PENDING
M11	Measurement Framework Established	Downstream	PENDING
M12	Project Closed	Downstream	PENDING

Milestone control: activity completion is not the same as output acceptance, which is not the same as milestone achievement.


8. STAGE-GATE CONTROL

Gate	Decision Point	Current Position	Status
G1	Project Baseline Approval	Established	PASSED
G2	Problem Validation	Established	PASSED
G3	Data Readiness	Suitable for current analytical use; controlled limitations remain	OPEN / CONTROLLED
G4	Insight Validation	Substantive evidence available; downstream disposition incomplete	PENDING
G5	Model Readiness	Candidate established; integration conditions remain	CONDITIONAL
G6	Intervention Readiness	Dependent on operational decision pathway	PENDING
G7	AI Readiness	Targeted validation completed; broader evidence remains	CONDITIONAL
G8	Integration Readiness	Critical interfaces unresolved	PENDING
G9	Solution Acceptance	Downstream	PENDING
G10	Implementation Decision	Downstream	PENDING
G11	Measurement Readiness	Downstream	PENDING
G12	Project Closure	Downstream	PENDING

Gate-control rule: a downstream gate shall not be advanced solely because its predecessor workstream has completed an activity. Required evidence must exist at the gate decision level.

9. SCHEDULE-DRIVING DEPENDENCIES

The schedule is currently governed by the following principal dependency chain:

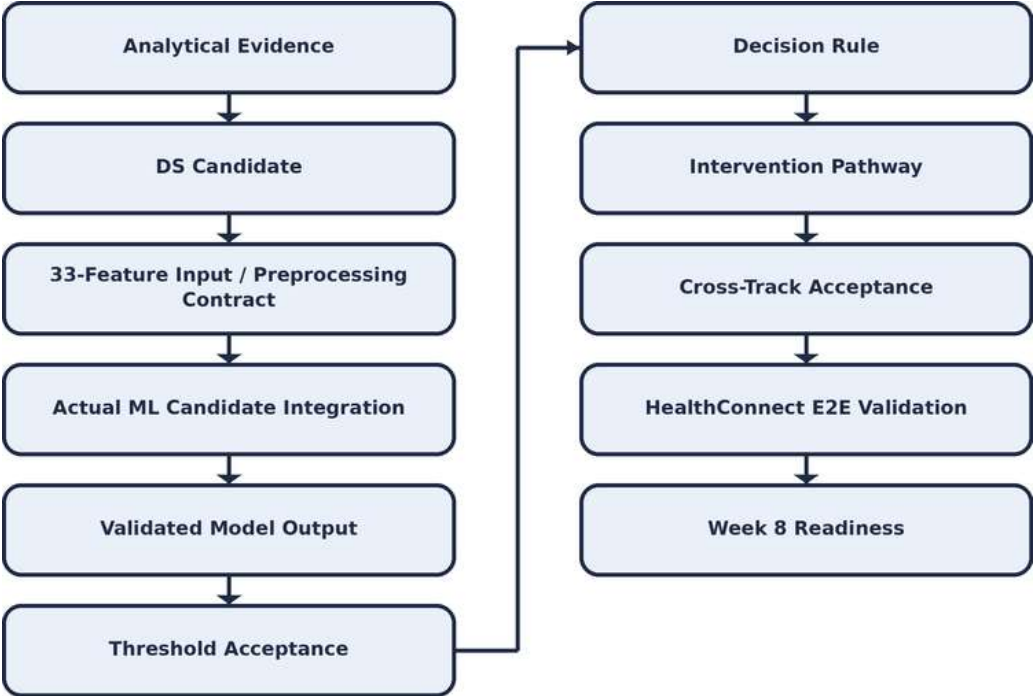

This sequence represents the current schedule-driving dependency structure.

It is not designated as a calculated critical path because the available schedule evidence does not contain sufficient activity-level durations and float values to support formal CPM analysis.

10. DEPENDENCY CONTROL REGISTER

ID	Predecessor	Successor	Current Condition	Schedule Effect
DEP-01	DS candidate	ML integration	Actual candidate transfer outstanding	Blocks actual candidate validation
DEP-02	33-feature structure	ML execution	Schema/preprocessing compatibility not reconciled	Blocks reliable candidate execution

ID	Predecessor	Successor	Current Condition	Schedule Effect
DEP-03	Model evidence	Threshold decision	Operational threshold not formally accepted	Blocks decision-rule validation
DEP-04	Accepted threshold	Decision/intervention	Score-to-action logic not validated	Blocks operational workflow validation
DEP-05	Dashboard evidence	Analytics acceptance	KPI reconciliation outstanding	Limits acceptance closure
DEP-06	Analytics findings	DS downstream use	Receiving-side disposition incomplete	Limits traceability
DEP-07	GenAI test environment	Remaining scenarios	Two planned scenarios affected by service availability	Prevents completion of those tests
DEP-08	Accepted interfaces	E2E workflow	Critical interfaces remain open	Blocks full E2E validation

Dependencies are controlled as schedule relationships. Their detailed issue, risk and corrective-action treatment remains in the relevant control registers.

11. CROSS-TRACK SCHEDULE POSITION

Interface	Required Schedule Outcome	Position	Control Effect
Analytics → DS	Analytical evidence received, assessed and dispositioned	Partially evidenced	Acceptance remains open
DS → ML	Actual candidate and input specification transferred and verified	Outstanding	Critical
ML → Decision	Validated score supports accepted classification logic	Outstanding	Critical
Decision → Intervention	Decision output maps to a testable intervention pathway	Outstanding	Critical
GenAI → HealthConnect	Safety, grounding, consistency and boundary evidence sufficient for intended use	Conditional	Controlled
All Tracks → Integrated Solution	Material interfaces operate coherently within HealthConnect workflow	Not demonstrated	Critical

12. WEEK 7 TESTING AND SCHEDULE INTERFACE

Week 7 testing has changed the scheduling basis from development completion to evidence-backed progression. The controlled sequence is:



This means a finding affecting a successor activity becomes a schedule condition until it is:

- Corrected and verified;
- Formally accepted with a documented residual limitation; or
- Otherwise dispositioned in accordance with the relevant control decision.

Testing therefore informs schedule progression but does not replace schedule control.

13. MATERIAL SCHEDULE CONSTRAINTS

SC-01 — DS→ML Candidate Transfer

The refined Data Science candidate has been established, but the actual candidate has not yet been demonstrated through the ML interface.

Control: *Maintain candidate integration as a prerequisite to downstream model acceptance.*

SC-02 — Input Structure Compatibility

The 33-feature candidate requires reconciliation of feature structure and preprocessing with the receiving ML interface.

Control: *Complete interface verification before treating candidate execution as validated.*

SC-03 — Operational Decision Rule

Model performance evidence does not itself establish an accepted operational threshold.

Control: *Obtain a controlled threshold decision before validating downstream classification behaviour.*

SC-04 — Intervention Pathway

The transition from model score to operational intervention remains unvalidated.

Control: *Treat score→decision→intervention as a distinct downstream validation activity.*

SC-05 — Analytics Acceptance

Dashboard evidence is available, but KPI reconciliation and downstream disposition remain incomplete.

Control: *Close the analytical acceptance condition before relying on the dashboard as fully accepted project evidence.*

SC-06 — GenAI Test Availability

Two planned scenarios were not executed because of Gemini service unavailability.

Control: *Re-execute when available or formally document their disposition; do not classify them as passed.*

SC-07 — GenAI Coverage

Selected safety and behavioural boundaries have been tested, but broader emergency, consistency and privacy-sensitive coverage remains incomplete.

Control: Maintain conditional readiness until the required evidence is obtained or formally dispositioned.

SC-08 — End-to-End Validation

The full HealthConnect workflow has not yet been validated across the relevant interfaces.

Control: Maintain E2E validation as a mandatory Week 8 activity.

14. SCHEDULE VARIANCE CONTROL

FORMAL WEEK 7 SCHEDULE VARIANCE: NOT ESTABLISHED

The available evidence does not support a defensible recalculation of:

- Planned versus actual activity duration;
- Milestone date variance;
- Float consumption;
- CPM critical-path movement; or
- Revised completion forecast.

Accordingly, no calendar variance is manufactured from dependency exposure.

The project does, however, have material forward schedule exposure because unresolved dependencies constrain several downstream activities.

Control Distinction

Condition	Schedule Interpretation
Dependency remains open	Schedule exposure
Successor cannot proceed	Controlled dependency blockage
Activity finishes later than approved date	Schedule variance
Float is consumed	Schedule impact
Critical-path date moves	Critical-path variance

Only the latter conditions can support a formal schedule-variance declaration when appropriately evidenced.

15. SCHEDULE-CRITICALITY POSITION

A formal CPM critical path is not calculated in this version.

The available schedule information is sufficient to identify the principal dependency chain, but not to calculate:

- Early Start;
- Early Finish;
- Late Start;
- Late Finish;
- Total Float; or
- Critical Path Method results.

The project shall therefore use the dependency chain for forward sequencing and escalation, without misrepresenting it as a mathematically calculated critical path.

16. WEEK 8 ENTRY CONTROL


The following conditions govern progression into final integration and validation.

ID	Requirement
EC-01	Actual DS candidate transferred to ML
EC-02	33-feature structure and preprocessing reconciled
EC-03	Actual candidate successfully executed
EC-04	Candidate scoring/output behaviour verified
EC-05	Operational threshold determined and controlled
EC-06	Score-to-decision logic defined and testable
EC-07	Decision-to-intervention pathway defined and testable
EC-08	Analytics reconciliation completed or formally dispositioned
EC-09	Analytics→DS downstream disposition established
EC-10	Outstanding GenAI scenarios executed or formally dispositioned
EC-11	Broader GenAI safety/consistency/privacy coverage completed or dispositioned
EC-12	Critical cross-track interface conditions cleared
EC-13	Material model limitations carried into acceptance/monitoring controls

ID	Requirement
EC-14	Risk, dependency, issue and decision records reconciled
EC-15	Full E2E validation is executable
EC-16	PM readiness assessment completed

These conditions control downstream progression. They do not prevent independent work from continuing where its own prerequisites are satisfied.

17. WEEK 8 DELIVERY SEQUENCE



Stage 1 — Interface Completion

DS candidate transfer → schema/preprocessing reconciliation → actual ML execution → receiving-side confirmation.

Stage 2 — Operationalisation

Threshold decision → score classification → decision rule → intervention pathway.

Stage 3 — Outstanding Validation

Analytics acceptance → GenAI scenario completion → safety/privacy/consistency validation → residual limitation assessment.

Stage 4 — Cross-Track Acceptance

Interface validation → finding disposition → corrective action → re-test → receiving-side acceptance.

Stage 5 — End-to-End Validation

Execute the integrated HealthConnect workflow and verify the interaction of the relevant solution components.

Stage 6 — Readiness Determination

Reconcile control records → assess outstanding conditions → determine readiness → authorise subsequent progression where evidence permits.

18. PARALLEL WORK CONTROL

The schedule deliberately avoids unnecessary serialisation.

Work Category	Activities	Treatment
Parallel	Analytics reconciliation, GenAI scenario work, PM control updates, documentation and independent technical refinement	Continue concurrently where prerequisites exist
Dependency-controlled	DS→ML integration, candidate execution, threshold determination	Await specified predecessor conditions
Sequential validation	Score→decision→intervention	Requires accepted model-output basis
Integrated validation	Full HealthConnect E2E testing	Requires material interface clearance
Gate-controlled	Solution acceptance, implementation readiness and closure	Requires defined acceptance evidence

19. SCHEDULE HEALTH ASSESSMENT

Dimension	RAG	Schedule Assessment
Scope / Architecture	GREEN	Approved project structure remains unchanged
Milestone Progression	AMBER-RED	Early milestones established; downstream milestones remain conditional
Dependencies	RED	Material cross-track dependencies remain unresolved
Technical Validation	AMBER-GREEN	Strong component-level evidence, particularly within ML
Cross-Track Integration	RED	Receiving-side acceptance remains incomplete
Testing Progression	AMBER	Substantial testing completed with defined outstanding conditions
GenAI Schedule Position	AMBER-RED	Evidence exists but coverage and service-availability constraints remain
Operational Integration	RED	Threshold, decision and intervention sequence not yet validated
E2E Validation	RED	Full HealthConnect workflow not yet executed
Schedule Variance	GREY	Formal calendar variance not established

Dimension	RAG	Schedule Assessment
Critical Path	GREY	CPM not calculated
Forward Progression	AMBER-RED	Week 8 progression is possible under controlled entry conditions

OVERALL SCHEDULE HEALTH: AMBER – RED

20. FORWARD MILESTONE OUTLOOK

Milestone	Forward Schedule Position	Primary Condition
M03	Controlled continuation	Formal data-readiness position
M04	Move toward acceptance	Analytical reconciliation and downstream disposition
M05	Complete candidate acceptance pathway	Actual DS→ML integration
M06	Progress toward operational definition	Decision and intervention logic
M07	Controlled completion	Outstanding GenAI validation
M08	Week 8 priority	Actual cross-track integration
M09	Downstream	Integrated validation and material finding disposition
M10	Downstream	Solution acceptance and residual-risk assessment
M11	Downstream	Accepted solution and measurement basis
M12	Downstream	Deliverable acceptance and closure

21. SCHEDULE CHANGE CONTROL

Any proposed material change to the approved schedule shall be assessed for:

- Milestone impact;
- Predecessor/successor implications;
- Gate impact;

- Cross-track sequencing;
- Testing consequences;
- Evidence and quality implications;
- resource implications;
- Risk and dependency exposure; and
- Effect on the forward delivery horizon.

A material change shall be incorporated through controlled schedule revision.

Historical schedule positions shall not be retrospectively altered to align them with subsequent project outcomes unless an approved baseline change requires such treatment.

22. SCHEDULE GOVERNANCE

Project Management shall maintain the authoritative project-level schedule record covering:

- Milestone status;
- Gate position;
- Forward activity sequence;
- Predecessor/successor relationships;
- Schedule-driving dependencies;
- Material constraints;
- Schedule variance evidence;
- Approved schedule changes;
- Week 8 entry conditions; and
- Version integrity.

Workstream owners remain accountable for delivery of their assigned outputs and supporting evidence.

PM is responsible for determining whether a workstream condition has a material project-level schedule consequence and whether the affected successor may legitimately progress.

23. CONTROL DOCUMENT INTERFACE

The schedule remains deliberately separated from the other project controls.

Document	Control Purpose
Updated Project Timeline & Schedule Control	Delivery sequence, milestones, gates and schedule dependencies
Testing Activity Tracker	Individual test execution and status
Integration & Issue Log	Materialised interface conditions and resolution
Risk & Dependency Register	Potential/project-level exposure and dependency treatment
Decision Log	Controlled decisions and acceptance positions
Cross-Track Validation & Acceptance Matrix	Receiving-side interface validation and acceptance
Testing Progress & Status Report	Week 7 testing progress and management position
Week 8 Readiness Assessment	Formal progression and readiness determination

Where the same condition appears across documents, each record serves a different control purpose. The timeline records its schedule consequence, rather than reproducing the underlying issue, risk or test record.

24. CURRENT SCHEDULE DETERMINATION

AMBER – RED — CONTROLLED WITH MATERIAL INTEGRATION DEPENDENCIES

The Week 7 schedule position demonstrates substantive progression from component development toward controlled cross-track validation.

The principal scheduling constraint is no longer the existence of individual workstream outputs. It is the successful progression of those outputs through their dependent interfaces into an accepted integrated workflow.

The immediate schedule-driving sequence is:



The project may progress into Week 8 under controlled conditions, but downstream milestone and gate achievement shall remain subject to the completion and verification of the applicable predecessor conditions.

No formal project-wide calendar delay is declared because the available evidence does not establish a defensible schedule variance or CPM movement.

25. VERSION CONTROL

Version	Reporting Point	Status	Controlled Change
1.0	Initial Planning	Baseline	Established WBS-derived delivery architecture, M01–M12 and G1–G12
2.0	Week 5	Execution Baseline	Added milestone execution position and dependency monitoring
3.0	Week 6	Controlled	Reassessed milestone maturity, gate position, dependencies, constraints and Week 7 forward sequence
4.0	Week 7	Current	Reassessed schedule following testing and refinement; incorporated cross-track acceptance conditions, actual DS→ML integration dependency, operationalisation sequence, GenAI validation constraints, E2E requirements and Week 8 entry controls

Current Control Record

Field	Value
Version	4.0
Reporting Period	Week 7
Schedule Health	AMBER-RED
Schedule Owner	Project Management
Primary Schedule Driver	Cross-track integration and acceptance dependencies
Formal Schedule Variance	Not established
Formal CPM Critical Path	Not calculated
Week 8 Position	Controlled progression subject to mandatory entry conditions
Next Formal Schedule Review	Week 8
