

ANALYSTLAB AFRICA
EXPERIENCE LAB INTERNSHIP PROGRAMME
HEALTHCONNECT CLINIC EXPERIENCE LAB
WEEK 6 — CROSS-TRACK COORDINATION RECORD

Improving Patient Appointment Attendance and Healthcare Support Using Data and AI

Field	Detail
Project	Improving Patient Appointment Attendance and Healthcare Support Using Data and AI
Programme	AnalystLab Africa Experience Lab
Function	Project Management
Reporting Period	Week 6
Document Status	Controlled Working Record
Version	1.0
Record Owner	Project Management
Review Point	Week 6 Integration Review

AMBER — ACTIVE COORDINATION WITH PENDING EVIDENCE

1. Record Purpose

This record establishes the formal evidence trail for material coordination undertaken between the HealthConnect workstreams during Week 6.

It records what was coordinated, between whom, what was exchanged, how the receiving workstream used the output, what changed as a result, what evidence supports the interaction, and what remains outstanding.

The record is specifically concerned with the interfaces between:

- Data Analytics
- Data Science
- Machine Learning / ML Engineering
- Generative AI

Project Management coordination is included where workstream evidence materially affected integration control, readiness, escalation or project-level decision-making.

This document does not replace the Integration & Dependency Register, Integration Issue Log or Decision Log. It provides the execution-level evidence of coordination occurring across those controlled interfaces.

2. Coordination Control Basis

A coordination activity is considered substantively evidenced only where the available record can establish, to the extent applicable, the following chain:



Coordination Status

Status	Control Meaning
Engaged	Coordination activity or substantive exchange occurred.
Transferred	A defined output was provided to the receiving party.
Incorporated	The receiving workstream demonstrably used or acted upon the transferred output.
Integrated	The resulting downstream change is evidenced within the receiving component or workflow.
Accepted	The receiving output satisfies the applicable acceptance condition.
Pending Evidence	Coordination is reported or initiated, but the evidence required to establish downstream incorporation or effect is incomplete.
Not Activated	The interface was not required or activated during the reporting period.

Control rule: a reported communication or handoff is not recorded as integration unless downstream use and resulting change can be demonstrated.

3. Master Coordination Register

8	Interface	Coordination Objective	Output / Input Exchanged	Coordination Activity & Result	Evidence Position	Status	Outstanding Requirement	Readiness Effect
CTC-01	Analytics → DS	Transfer validated attendance evidence into predictive development	Validated findings, engineered features and Previous No-Show Rate	Analytics reported providing the refined analytical inputs for DS modelling. Downstream modelling continued using the revised analytical direction; the precise incorporation of each input is not yet fully traceable.	Exchange evidenced; receiver-side resulting change only partially evidenced.	Pending Evidence	Confirm which analytical inputs were incorporated and identify the resulting model artefact/change.	Prevents full closure of the Analytics→DS interface.
CTC-02	DS → ML	Transfer intended predictive candidate for technical implementation	Candidate model / implementation package	Intended candidate was not transferred during the review period. ML instead used a Random Forest stand-in to exercise the integration pathway.	Technical pathway evidenced; intended cross-track handoff not evidenced.	Transferred — Pending	Complete actual candidate-model handoff and repeat integration verification.	Primary outstanding technical interface for Week 7.
CTC-03	ML → Downstream Solution	Establish technically usable scoring capability	Batch risk-score output and scoring interface	ML completed batch scoring against a 5,000-row dataset and a 60-row simulated upcoming batch, with schema, row-count, output-range and reproducibility checks.	Strong technical evidence; operational use not established.	Integrated Component	Define and accept operational interpretation and decision conditions for risk scores.	Technical readiness established; operational readiness remains conditional.
CTC-04	GenAI → PM / Governance	Convert testing evidence into project control	Scenario-testing results covering safety, refusal, escalation and pricing boundaries	Scenario testing exposed inconsistent emergency-disclaimer behaviour, which was carried into the Integration Issue Log for targeted refinement and retesting.	Specific behavioural evidence available.	Incorporated	Complete targeted retest and establish consistency across relevant scenarios.	Supports controlled, rather than unconditional, Week 7 readiness.
CTC-05	GenAI → Validation	Establish evidence for support behaviour and safety boundaries	Tested assistant responses and refinement requirements	Five scenario categories were exercised, establishing evidence for selected behaviours but not broad behavioural reliability across conversational conditions.	Evidence is substantive but scoped.	Partially Established	Expand targeted scenario/regression coverage and document residual limitations.	Validation remains conditional.
CTC-06	Analytics → PM / Project Control	Convert analytical findings into controlled project inputs	Statistical findings, revised interpretations, confidence intervals and interaction analysis	PM incorporated the analytical evidence into integration, issue and decision controls, including explicit distinction between association and causality.	Direct project-control incorporation evidenced.	Integrated into PM Control	Preserve interpretation boundaries as findings move downstream.	Strengthens evidence quality and downstream control.
CTC-07	ML → PM / Project Control	Establish technical evidence for integration readiness	Integration tests, scoring outputs, schema alignment, reproducibility and resolved interface defects	PM reviewed ML evidence and incorporated the resulting readiness position into project controls.	Strong technical evidence available.	Integrated into PM Control	Reassess following integration of the actual DS candidate.	Supports technical readiness assessment but not full solution readiness.

8	Interface	Coordination Objective	Output / Input Exchanged	Coordination Activity & Result	Evidence Position	Status	Outstanding Requirement	Readiness Effect
CTC-08	DS → PM / Project Control	Establish predictive-development position for integration planning	Binary target direction, engineered features, candidate configurations and model-development preparation	PM incorporated the DS development position into dependency, issue and readiness control. Comparative model results and final candidate selection remain outstanding.	Development evidence available; final-result evidence incomplete.	Incorporated	Execute comparative evaluation and record candidate-selection decision.	Limits DS→ML handoff readiness.
CTC-09	All Workstreams → PM	Consolidate cross-track status and interface evidence	Workstream outputs, status, dependencies, issues and readiness information	PM consolidated available workstream evidence into the controlled integration record and associated project controls.	Project-level consolidation evidenced.	Integrated into PM Control	Maintain evidence updates at subsequent checkpoints.	Enables controlled transition into Week 7.

4. Detailed Coordination Records

The overview below shows how the nine coordination interfaces relate: a technical pipeline from Analytics through Data Science and ML into the downstream scoring component, a parallel GenAI → Validation track, and a consolidation of all four workstreams into PM / Project Control ahead of the Week 7 readiness position.

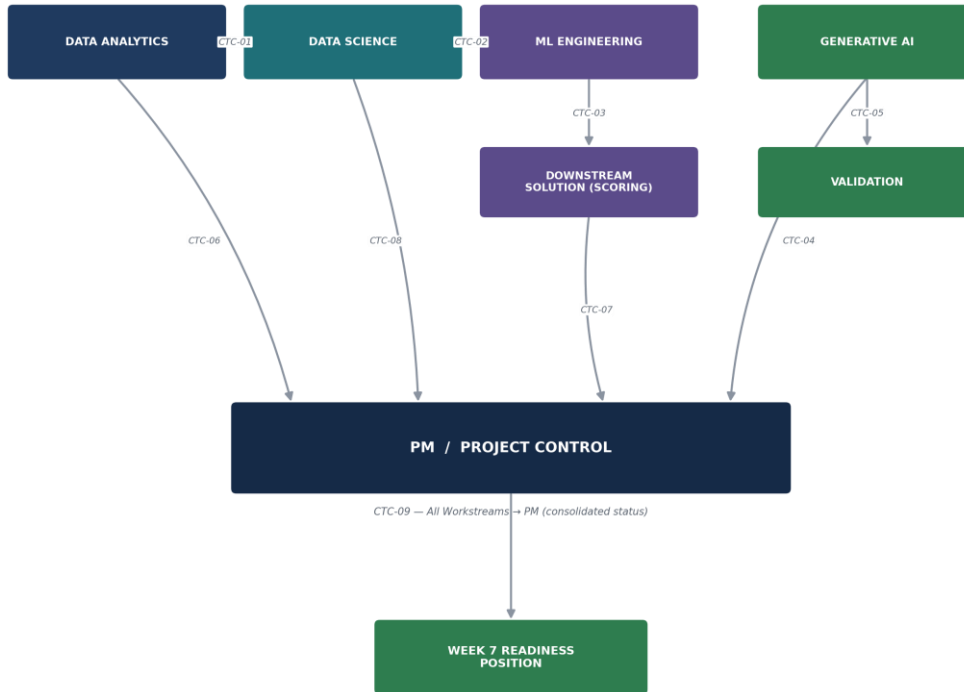


Figure 4.1 — Week 6 coordination flow across the nine controlled interfaces (CTC-01 to CTC-09)

CTC-01 — Data Analytics → Data Science

Coordination Objective: Move validated attendance and no-show evidence beyond descriptive analysis into predictive model development.

Output / Input Exchanged: Validated attendance/no-show findings, relevant engineered features, and the Previous No-Show Rate measure.

Coordination Activity: The analytical workstream progressed from the Week 5 EDA baseline to statistically supported findings and revised interpretations. The resulting analytical inputs were made available to Data Science for predictive development.

Resulting Change: Data Science continued predictive development using the revised analytical direction. However, the available evidence does not yet identify, input by input, how the analytical outputs changed the resulting candidate model.

Evidence Assessment: The exchange is evidenced. The downstream incorporation is not yet sufficiently traceable to classify the interface as fully integrated.

Current Status: Pending Evidence

Outstanding Action / Required Closure Evidence: Receiver-side confirmation should establish: (1) the analytical inputs incorporated; (2) the corresponding model or feature artefact affected; and (3) the resulting change attributable to the handoff.

Readiness Impact: Analytics→DS interface remains partially evidenced.

CTC-02 — Data Science → ML Engineering

Coordination Objective: Transfer the intended predictive candidate into the ML implementation pathway.

Output / Input Exchanged: Data Science candidate model and associated implementation requirements.

Coordination Activity: The intended DS candidate was not transferred during the reviewed period. ML nevertheless exercised its implementation pathway using a Random Forest stand-in.

Resulting Change: ML demonstrated that its model wrapper and batch-scoring pathway could support an alternative estimator and successfully addressed interface defects encountered during integration testing. This established technical pathway readiness, but did not establish integration of the intended Data Science candidate.

Evidence Assessment: The ML technical pathway is evidenced. The actual DS→ML handoff is not.

Current Status: Transfer Pending

Outstanding Action / Required Closure Evidence: Actual DS candidate received; receiver acceptance confirmed; candidate integrated into ML pathway; integration tests repeated against the intended candidate; resulting metrics/outputs recorded.

Readiness Impact: Material Week 7 integration dependency.

CTC-03 — ML Engineering → Downstream Solution

Coordination Objective: Demonstrate that the predictive component can produce usable technical outputs beyond model training.

Output / Input Exchanged: Batch risk scores generated through the ML scoring pathway.

Coordination Activity: ML completed end-to-end batch scoring against a 5,000-row dataset and a 60-row simulated upcoming batch. Schema alignment, output range, NaN and row-count checks were incorporated alongside integration testing and reproducibility checks.

Resulting Change: The workstream progressed from a training-time pipeline to a technically demonstrated scoring-capable component.

Evidence Assessment: The evidence establishes technical scoring capability. It does not establish accepted operational thresholds, intervention rules or production workflow use.

Current Status: Integrated Component

Outstanding Action / Required Closure Evidence: Define and accept the operational interpretation of the generated risk scores.

Readiness Impact: Technical readiness is ahead of operational readiness.

CTC-04 — Generative AI → PM / Governance

Coordination Objective: Translate GenAI testing evidence into controlled project-level readiness and issue management.

Output / Input Exchanged: Scenario-testing evidence covering diagnosis-related refusal, emergency escalation, pricing redirection, absence of invented pricing, and treatment/medication boundaries.

Coordination Activity: PM reviewed the testing evidence against project safety and readiness controls. An inconsistent emergency-disclaimer response was identified and formally carried forward as an open integration issue.

Resulting Change: The testing evidence directly affected project control by preventing premature closure of the GenAI readiness position.

Evidence Assessment: Specific behavioural evidence is available and has been incorporated into the Integration Issue Log.

Current Status: Incorporated into PM Control

Outstanding Action / Required Closure Evidence: Targeted retest of the disclaimer behaviour.

Readiness Impact: GenAI remains conditionally ready for Week 7 testing and refinement.

CTC-05 — Generative AI → Validation

Coordination Objective: Establish whether current GenAI behaviour provides sufficient evidence for progression into broader validation.

Output / Input Exchanged: Tested assistant responses across defined behavioural categories and associated refinement requirements.

Coordination Activity: Live scenario testing was conducted across defined behavioural categories.

Resulting Change: Evidence was established for selected expected behaviours. However, the testing set remains insufficient to establish broad behavioural reliability across indirect, ambiguous or more complex conversational conditions.

The record supports scoped behavioural evidence but does not yet support broad behavioural validation.

Evidence Assessment: Evidence is substantive but scoped.

Current Status: Partially Established

Outstanding Action / Required Closure Evidence: Extend targeted regression and edge-case testing during Week 7.

Readiness Impact: Validation remains conditional.

CTC-06 — Data Analytics → PM / Project Control

Coordination Objective: Ensure material analytical evidence is incorporated into project-level control without overstating its evidentiary strength.

Output / Input Exchanged: Statistical findings, revised interpretations, confidence intervals and interaction analysis.

Coordination Activity: PM reviewed the analytical evidence produced during Week 6 and incorporated it into the Integration & Dependency Register, Integration Issue Log and Decision Log, explicitly distinguishing statistical association from causal or intervention-effect claims.

Resulting Change: Analytical findings are now embedded in controlled project records rather than standing only as workstream output.

Evidence Assessment: Direct project-control incorporation is evidenced.

Current Status: Integrated into PM Control

Outstanding Action / Required Closure Evidence: Preserve the association-versus-causality interpretation boundary as findings continue to move downstream into modelling, intervention design and reporting.

Readiness Impact: Strengthens evidence quality and downstream decision governance without asserting unproven causal effects.

CTC-07 — ML Engineering → PM / Project Control

Coordination Objective: Establish technical evidence for integration and readiness assessment at the project level.

Output / Input Exchanged: Integration test results, batch-scoring outputs, schema-alignment checks, reproducibility evidence and records of resolved interface defects.

Coordination Activity: PM reviewed the ML technical evidence and incorporated the resulting readiness position into the Integration & Dependency Register and Integration Issue Log.

Resulting Change: ML's technical pathway readiness is now a controlled project position rather than an internal workstream claim.

Evidence Assessment: Strong technical evidence is available and directly incorporated.

Current Status: Integrated into PM Control

Outstanding Action / Required Closure Evidence: Reassess the readiness position once the actual Data Science candidate is integrated (see CTC-02).

Readiness Impact: Supports a technical readiness assessment but does not, by itself, establish full solution readiness.

CTC-08 — Data Science → PM / Project Control

Coordination Objective: Establish a controlled predictive-development position to inform integration planning.

Output / Input Exchanged: Binary target direction, engineered features, candidate model configurations and model-development preparation evidence.

Coordination Activity: PM incorporated the DS development position into the Integration & Dependency Register, Integration Issue Log and Decision Log.

Resulting Change: The predictive-development status is now formally tracked as a project control position rather than only an internal development record.

Evidence Assessment: Development evidence is available; comparative execution and final-candidate evidence remain incomplete.

Current Status: Incorporated

Outstanding Action / Required Closure Evidence: Execute comparative evaluation and record the candidate-selection decision (see DEC-10).

Readiness Impact: Limits the DS→ML handoff (CTC-02) until a final candidate is selected and transferred.

CTC-09 — All Workstreams → PM

Coordination Objective: Consolidate cross-track status, dependencies, issues and readiness information into a single controlled project position.

Output / Input Exchanged: Workstream outputs, status updates, dependency positions, issue evidence and readiness information from Analytics, Data Science, ML and Generative AI.

Coordination Activity: PM consolidated the available Week 6 workstream evidence into the Integration & Dependency Register, Integration Issue Log, Decision Log and this Coordination Record.

Resulting Change: A single, evidence-based Week 6 project position has been established across all controlled workstream interfaces.

Evidence Assessment: Project-level consolidation is directly evidenced by the four controlled records themselves.

Current Status: Integrated into PM Control

Outstanding Action / Required Closure Evidence: Maintain evidence updates at each subsequent Week 7 integration checkpoint.

Readiness Impact: Enables a controlled, evidence-based transition into Week 7 rather than an assumed one.

5. Week 6 Coordination Position

OVERALL COORDINATION POSITION: AMBER — ACTIVE COORDINATION WITH PENDING EVIDENCE

Week 6 evidences substantive coordination across all four technical workstreams and their consolidation into Project Management control. No interface is inactive, and no coordination attempt has failed outright.

Principal coordination gaps

- Analytics → DS incorporation is reported but not yet traceable to a specific resulting model change (CTC-01);
- the intended DS → ML candidate handoff has not occurred; ML integration evidence rests on a stand-in estimator (CTC-02);
- GenAI → Validation evidence is scoped to five categories and does not yet establish broad behavioural reliability (CTC-05).

These gaps represent coordination dependencies for Week 7, not a breakdown in cross-track coordination. Each interface has been actively engaged; what remains outstanding is the evidence needed to classify several interfaces as fully integrated rather than merely transferred or incorporated.

6. Governance and Maintenance

Control	Requirement
Record Owner	Project Management
Review Point	Week 6 Integration Review; subsequent Week 7 coordination checkpoints
Update Triggers	New coordination activity, change in evidence status, receiver-side confirmation, escalation, or change to Week 7 readiness
Evidence Basis	Workstream-reported exchange, receiver confirmation, technical test evidence, or other traceable coordination artefact

Control	Requirement
Cross-References	Integration & Dependency Register, Integration Issue Log, Decision Log and underlying workstream evidence

This record provides execution-level evidence of coordination; it does not itself carry escalation or closure authority. Material consequences arising from a coordination gap are escalated through the Integration & Dependency Register, Integration Issue Log or Decision Log as applicable.

7. Version Control

Version	Phase	Change
V1.0	Week 6	Initial Cross-Track Coordination Record established from verified Week 6 workstream evidence
Next Review	Week 7	Reassess coordination status, incorporate receiver-side confirmations and update readiness effects

Next formal review: Week 7 PM integration checkpoint, or earlier where a coordination gap materially affects integration, testing, scope or readiness.
