

ANALYSTLAB AFRICA
EXPERIENCE LAB INTERNSHIP PROGRAMME
HEALTHCONNECT CLINIC EXPERIENCE LAB
WEEK 6 — DECISION LOG

Improving Patient Appointment Attendance and Healthcare Support Using Data and AI

Field	Detail
Project	Improving Patient Appointment Attendance and Healthcare Support Using Data and AI
Programme	AnalystLab Africa Experience Lab
Track	Project Management
Project Phase	Solution Development & Integration
Reporting Period	Week 6
Version	2.0
Decision Log Owner	Project Management Function
Review Authority	Project Sponsor / Project Leadership
Status	Active

AMBER — CONTROLLED WITH MATERIAL PENDING DECISIONS

1. Decision Control Purpose

This log provides the authoritative Project Management record of material decisions affecting scope, solution direction, cross-workstream integration, evidence interpretation, acceptance, readiness, or downstream delivery during Week 6.

It records both:

- Confirmed Decisions — decisions for which the available project evidence establishes an adopted direction; and
- Pending Decision Points — matters requiring formal resolution before a dependent activity or project position can be treated as fully controlled.

The log does not replace workstream-level technical records. Routine implementation choices remain with the responsible workstream unless they materially affect another workstream, project control, acceptance or delivery readiness.

2. Decision Record Standard

Every material decision is controlled through the following traceability chain:



Where a decision has not yet been formally resolved, the record terminates at:



A decision is therefore not considered implemented merely because it has been discussed or recorded.

Decision Status

Status	Meaning
Confirmed	Direction has been adopted and is supported by available project evidence
In Implementation	Decision is established and resulting action is underway
Pending	Material decision point identified; resolution not yet evidenced
Under Review	Previously adopted direction is being reassessed against new evidence
Superseded	Replaced by a subsequent decision
Closed	Implementation and required downstream verification completed

3. Master Decision Register

ID	Decision Subject	Trigger / Decision Point	Evidence Basis	Decision / Current Position	Rationale	Material Impact	Implementation / Required Action	Owner / Authority	Status	Traceability
DEC-01	Predictive target definition	Initial approach used three outcome classes; Week 6 shifted toward the primary attendance objective.	Week 5/6 Data Science development direction.	Binary Attended vs No-Show classification adopted for current predictive development. Treatment of Cancelled records remains unresolved.	Directs the predictive objective toward appointment attendance while simplifying the immediate classification problem.	Scope / Model Definition / Integration	Document treatment of Cancelled records and ensure the final target definition is consistent across DS and ML artefacts.	Data Science; scope confirmation from Project Leadership where required	In Implementation	II-07 / D-07 / D-13
DEC-02	Waiting-time variable	Earlier work considered waiting time as potentially predictive; subsequent evidence did not support it.	Revised Analytics conclusions and downstream feature review.	Waiting time is not retained as an established predictive driver on the current evidence base.	Prevents an insufficiently supported variable from being carried forward as a validated project finding.	Evidence Quality / Model Input	Remove or qualify unsupported predictive interpretation across downstream artefacts.	Data Analytics / PM evidence control	In Implementation	D-05 / II-08
DEC-03	Interpretation of distance finding	The 30–40 km segment showed elevated no-show behaviour, creating a risk of causal interpretation.	Statistical analysis and interaction findings from Week 6.	Distance is treated as an associated/logistical signal, not established causality.	Current evidence supports association but does not establish a causal mechanism.	Evidence Quality / Decision Governance	Maintain qualified interpretation in downstream modelling, intervention and reporting materials.	Data Analytics / PM governance	In Implementation	II-08
DEC-04	“No Reminder” data treatment	Reminder information required interpretation during data preparation.	Week 6 data preparation and validation.	“No Reminder” is retained as a meaningful category rather than treated as a missing value.	The category represents an observable process condition with potential analytical relevance.	Data Quality / Downstream Consistency	Preserve the treatment through relevant analytical and modelling pipelines.	Data Analytics / Data Science	Confirmed	D-03 / D-04
DEC-05	GenAI test-model transition	The previously referenced Gemini model was retired, requiring the testing configuration to change.	GenAI testing environment and model availability.	Testing moved to the current supported model alias.	Maintains test continuity following model retirement. The change itself is not evidence of performance improvement.	Testing Continuity / Evidence Comparability	Record model/version context for subsequent regression and safety evidence.	GenAI	Confirmed	II-01 / II-03

ID	Decision Subject	Trigger / Decision Point	Evidence Basis	Decision / Current Position	Rationale	Material Impact	Implementation / Required Action	Owner / Authority	Status	Traceability
DEC-06	ML integration test approach	The intended DS candidate model was not available for actual ML integration during the review period.	ML integration artefacts, test results and outstanding DS handoff.	A Random Forest stand-in was used to verify the ML integration and batch-scoring pathway.	Allows the interface and scoring pathway to be tested without misrepresenting the stand-in as the final project model.	Integration / Schedule / Readiness	Replace stand-in with the approved DS candidate and repeat applicable integration verification.	ML / Data Science	In Implementation	II-04 / D-07 / D-14
DEC-07	Technical versus operational readiness	ML demonstrated scoring capability, but operational thresholds and workflow use were not established.	ML Week 6 integration evidence.	Technical scoring capability will not be treated as operational readiness.	Separates component capability from accepted operational use.	Integration / Operational Readiness	Define intended score interpretation and operational decision conditions before operational readiness is claimed.	PM / relevant downstream authority	Confirmed	II-09 / D-14 / D-16
DEC-08	GenAI disclaimer inconsistency	Scenario testing identified inconsistent emergency-disclaimer behaviour.	GenAI test evidence; II-01.	The inconsistency remains subject to targeted refinement and retesting; it is not treated as closed.	Evidence establishes a behavioural inconsistency requiring verification, but not a confirmed safety incident.	Safety Governance / Validation Readiness	Execute targeted retest and verify expected behaviour against agreed acceptance conditions.	GenAI / PM oversight	In Implementation	II-01 / D-15
DEC-09	Interpretation boundary for analytical findings	Statistical validation strengthened the evidence base but did not establish causal or intervention effects.	Chi-square/Z-tests, confidence intervals and interaction analysis.	Statistically supported findings may inform modelling and intervention hypotheses but must not be represented as causal or intervention-effect evidence without further validation.	Preserves the distinction between statistical association, predictive evidence and causal inference.	Evidence Governance / Downstream Decision Quality	Apply the evidence boundary consistently across integrated outputs.	Data Analytics / PM	Confirmed	II-08 / D-05
DEC-10	Final predictive candidate	Multiple candidate configurations were prepared, but comparative execution evidence was not available at review.	Data Science Week 6 development artefacts.	Final predictive candidate selection remains pending.	Selecting a model without comparative execution and selection evidence would create an unsupported project decision.	Model Readiness / DS→ML Integration	Execute comparative evaluation, document selection rationale and formally identify the candidate for transfer.	Data Science; escalation to Project Leadership if required	Pending	II-05 / D-07 / D-13
DEC-11	Analytics → DS handoff acceptance	Analytics reported transfer of validated findings/features, but downstream incorporation was not fully traceable.	Analytics handoff report and available downstream evidence.	The handoff is not treated as fully accepted until receiver-side incorporation and resulting change are evidenced.	Communication establishes exchange; it does not independently establish acceptance or integration.	Integration / Traceability	Obtain receiver confirmation and identify the incorporated analytical inputs and resulting downstream change.	PM / Data Science	Pending	II-06 / D-05 / D-12

ID	Decision Subject	Trigger / Decision Point	Evidence Basis	Decision / Current Position	Rationale	Material Impact	Implementation / Required Action	Owner / Authority	Status	Traceability
DEC-12	Operational use of ML risk scores	ML produced risk-score outputs without an established operational threshold or intervention rule.	ML batch-scoring evidence and operational-readiness review.	Operational use of risk scores remains pending formal definition and acceptance.	A technically generated score is not, by itself, an operational decision mechanism.	Operational Integration / Readiness	Define intended use, interpretation, threshold/decision conditions and receiving workflow before operational acceptance.	Project Leadership / relevant downstream function	Pending	II-09 / D-14 / D-16

4. Decision Authority and Evidence Integrity

The available Week 6 material does not establish a separate formal approval record for every technical direction above. Accordingly, this log distinguishes between:

- direction evidenced through workstream execution;
- PM governance positions established to control downstream use; and
- decisions requiring formal confirmation by the appropriate authority.

Where formal authority or approval evidence is absent, the item is not retrospectively represented as a sponsor-approved decision.

This is particularly relevant to DEC-01, DEC-10, DEC-11 and DEC-12, where downstream scope, model selection or operational use requires a level of confirmation beyond simply observing that development activity has taken place.

5. Decision Dependency Map

Material decisions do not operate independently. Their downstream sequence — with the Analytics and GenAI decision chains progressing in parallel before merging back into the primary path — is shown below.

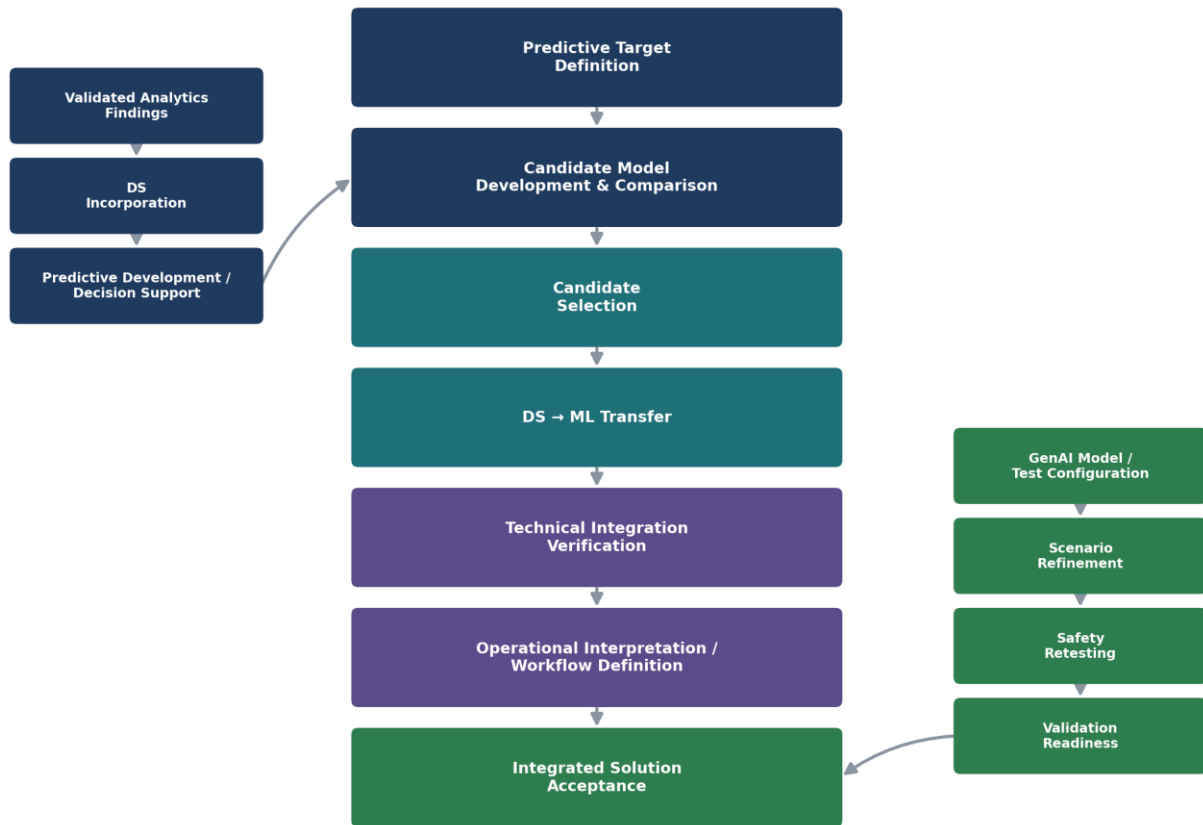


Figure 5.1 — Decision dependency map: the Analytics chain merges into candidate model development; the GenAI chain merges into integrated solution acceptance

This establishes where decision latency can become a downstream integration constraint.

6. Decision Impact Control

Material decisions are assessed against the following control dimensions:

Dimension	Control Question
Scope	Does the decision alter the problem definition, target, deliverable or intended use?
Integration	Does it change an input, output, interface or acceptance condition between workstreams?
Schedule	Can implementation or delayed resolution affect sequencing, milestones or testing?
Quality	Does it alter evidence reliability, interpretation, safety or acceptance?
Readiness	Does it enable or prevent progression to the next project stage?

A decision with material downstream impact must trigger review of the relevant risk, dependency, issue and/or schedule control.

7. Decision Implementation Control

For confirmed decisions, implementation is tracked separately from the decision itself:



A decision remains In Implementation where the direction is established but the resulting project change has not yet been verified. It becomes Closed only when the required implementation and downstream verification are complete.

This prevents the log from treating a documented decision as equivalent to completed delivery.

8. Pending Decision Control

The following decisions remain material to downstream integration:

ID	Decision Required	Consequence if Deferred	Required Resolution
DEC-10	Select the final predictive candidate.	DS→ML integration cannot be completed using the intended model.	Comparative performance evidence and selection rationale.
DEC-11	Confirm acceptance and incorporation of Analytics→DS outputs.	Analytical integration remains only partially evidenced.	Receiver-side confirmation and traceable resulting change.
DEC-12	Define operational use of ML risk scores.	Technical output cannot progress to accepted operational decision use.	Agreed interpretation, thresholds/decision conditions and workflow acceptance.
DEC-01 clarification	Confirm treatment of Cancelled records in the binary target.	Target definition remains potentially inconsistent across modelling artefacts.	Documented treatment and rationale.

Decision latency control: any pending decision that begins to constrain a dependent workstream, milestone or Week 7 test condition should be escalated through the appropriate project control.

9. Decision Review and Reversal Triggers

A confirmed decision should be revisited where:

- new evidence materially changes its original rationale;

- an implementation constraint invalidates the assumed approach;
- a downstream workstream demonstrates incompatibility;
- a material risk or issue emerges from implementation;
- approved scope or requirements change;
- the decision produces an unintended quality, safety or operational consequence; or
- a subsequent decision supersedes the original direction.

A review does not automatically invalidate the original decision; the original record remains preserved for traceability.

10. Week 6 Decision Position

OVERALL DECISION POSITION: AMBER — CONTROLLED WITH MATERIAL PENDING DECISIONS

Week 6 has established several working directions governing predictive modelling, analytical interpretation, data treatment, GenAI testing and the separation of technical capability from operational readiness.

Principal unresolved decision points

- final predictive candidate selection;
- formal confirmation of the Analytics → DS downstream handoff;
- treatment of Cancelled records within the binary modelling target; and
- operational interpretation and use of ML risk scores.

These do not constitute a project-wide decision blockage at the current stage. They do, however, represent decision dependencies for downstream integration and readiness and should remain actively controlled into Week 7.

11. Governance and Record Integrity

Control	Requirement
Decision Log Owner	Project Management Function
Review Authority	Project Sponsor / Project Leadership
Review Frequency	Weekly PM control review and material integration checkpoints
Update Triggers	New material decision, decision status change, implementation evidence, unresolved decision latency, scope change, new evidence or downstream consequence

Control	Requirement
Decision Evidence	Approved artefact, documented workstream confirmation, meeting/decision record, accepted deliverable or other traceable project evidence
Escalation Authority	Project Leadership
Cross-References	Integration Issue Log, Integration & Dependency Register, Risk & Dependency Register, Project Schedule and workstream evidence

The Decision Log serves as the single PM record for material project decisions. Detailed technical implementation records remain under the control of the relevant workstream.

No decision should be marked closed without sufficient evidence of implementation and, where applicable, downstream acceptance.

12. Version Control

Version	Phase	Change
V1.0	Week 6	Initial decision control established from verified Week 6 workstream evidence
V2.0	Week 6	Decision records consolidated, decision authority/evidence boundaries strengthened, pending decisions separated from confirmed decisions, and cross-control traceability established
Next Review	Week 7	Reassess pending decisions, implementation status, downstream verification and newly arising material decisions

Next formal review: Week 7 PM integration checkpoint, or earlier where decision latency materially affects integration, testing, scope or readiness.
